ОРГАНИЗАЦИЯ ОБЪЕДИНЕННЫХ НАЦИЙ

EP

Программа Организации Объединенных Наций по окружающей среде

Distr.
GENERAL

UNEP/OzL.Pro/ExCom/99/16
29 October 2026

RUSSIAN
ORIGINAL: ENGLISH

ИСПОЛНИТЕЛЬНЫЙ КОМИТЕТ
МНОГОСТОРОННЕГО ФОНДА ДЛЯ
ОСУЩЕСТВЛЕНИЯ МОНРЕАЛЬСКОГО ПРОТОКОЛА
Девяносто девятое совещание
Монреаль, 7–11 декабря 2026 года
Пункт 7 a) iv) предварительной повестки дня[1]

ОТЧЕТ О ХОДЕ РАБОТЫ ЮНЕП ПО СОСТОЯНИЮ НА 31 ДЕКАБРЯ 2025 ГОДА

Введение

1. В настоящем документе представлен отчет о ходе работы ЮНЕП по состоянию на 31 декабря 2025 года[2].

2. Доклад о ходе работы ЮНЕП включает проверенную Секретариатом информацию о ходе реализации текущих проектов по каждой стране, принимая во внимание задержки в реализации по сравнению с запланированными сроками завершения, о которых было сообщено в 2025 году, потенциальное воздействие этих задержек на поэтапный отказ от регулируемых веществ и темпы запланированных выплат. Анализ, представленный в настоящем документе, основан на данных в тоннах ОРС для всех регулируемых веществ за исключением ГФУ, которые измеряются в метрических тоннах (т) и тоннах CO_2-экв.[3]

3. В настоящем документе приводится краткая информация о ходе реализации проектов на 2025 год и совокупно с 1991 года, и рассматриваются все регулируемые Монреальским протоколом вещества, включая вещества, приведенные в приложении F (ГФУ), в рамках всех проектов, утвержденных в рамках финансирования из регулярного бюджета и дополнительных добровольных взносов.[4] Он также содержит обзор статуса осуществления каждого реализуемого[5] проекта на

[1] UNEP/OzL.Pro/ExCom/99/1

[2] Отчет о ходе работы прилагается к настоящему документу. Данные включены в базу данных Сводного отчета о ходе работы, которая представлена на портале 99-го совещания, на веб-сайте Многостороннего фонда, в формате электронной таблицы Microsoft Excel.

[3] В соответствии с решением 84/12 a) iv), данные об измерении ГФУ в тоннах CO_2-экв. включены в отчеты о ходе работы, представленные 99-му совещанию.

[4] Финансируется 17 Сторонами, не действующими в рамках статьи 5, для обеспечения поддержки быстрому началу осуществления Кигалийской поправки.

[5] Реализуемые проекты — это все проекты, которые находились в стадии реализации по состоянию на 31 декабря 2025 года. Ключевые показатели хода реализации включают процент выделенных средств и процент проектов, по которым началась выплата средств; средства, которые, как ожидается, будут выделены до конца года, в процентах от утвержденного финансирования; среднюю продолжительность предполагаемой

Документы, подготовленные к совещанию Исполнительного комитета Многостороннего фонда для осуществления Монреальского протокола, не предрешают ни одного из решений, которые Исполнительный комитет может принять после выпуска документа.

страновом уровне. В нем указаны проекты с задержками в реализации и потенциальное воздействие задержек на поэтапный отказ от регулируемых веществ, а также проекты с неурегулированными вопросами для рассмотрения Исполнительным комитетом. Поскольку все проекты, утвержденные в рамках дополнительных добровольных взносов, завершены, а остатки средств будут возвращены в Фонд, Секретариат больше не будет отдельно отчитываться по этим проектам.

Ход реализации проектов на 2025 год и совокупно с 1991 года

4. По состоянию на 31 декабря 2025 года Исполнительный комитет утвердил проекты для ЮНЕП на сумму 521,47 млн долл. США, из которых 481,89 млн долл. США предназначены для реализации неинвестиционных проектов, а 39,58 млн долл. США — для покрытия вспомогательных расходов учреждения-исполнителя (за исключением отмененных и переданных проектов). В таблице 1 приводится краткая информация о реализации проектов с момента их создания до конца 2025 года.

Таблица 1. Краткая информация о проектах для ЮНЕП с момента создания Многостороннего фонда

Показатели	Совокупно с 1991 года*
Число утверждений	3 233
Число завершенных проектов	2 765
Общая сумма утвержденных средств (без учета вспомогательных расходов) (в долл. США)	481 887 196
Общая сумма выплаченных средств (без учета вспомогательных расходов) (в долл. США)	412 395 943
Всего утверждено к поэтапному отказу (в тоннах ОРС)**	2 718,8
Всего фактически осуществлено поэтапного отказа (в тоннах ОРС)**	2 283,0
Всего утверждено к поэтапному отказу (т)	873,4
Всего фактически осуществлено поэтапного отказа (т)	35,9
Всего утверждено к поэтапному отказу (в тоннах CO_2-экв.)***	1 826 294
Всего фактически осуществлено поэтапного отказа (в тоннах CO_2-экв.)***	68 058

* За исключением отмененных и переданных проектов.
** Включая только потребление.
*** Только для проектов, связанных с ГФУ (включая только потребление).

5. В 2025 году было одобрено 102 новых проекта и мероприятия. Ожидается, что этот уровень финансирования приведет к поэтапному отказу от потребления ОРВ в объеме 2 719 тонн ОРС и потребления ГФУ — в объеме 873 т (1 826 294 тонны CO_2-экв). В приложении I представлена информация о статусе реализации проектов по странам в 2025 году.

6. В таблице 2 представлен статус реализации проектов, включая выделение средств по типу проекта, по состоянию на 31 декабря 2025 года. В приложении II представлена аналитическая информация по годам, начиная с 1991 года.

задержки в реализации; а также информацию, представленную в колонке «Примечания» в базе данных отчетов о ходе работы.

Таблица 2. Статус реализации по типу проектов на 31 декабря 2025 года*

Тип	Количество проектов			Финансирование (в долл. США)**			
	Утверждено	Завершено	% завершения	Утверждено	Выплачено	Баланс	% выплат
Программа учреждения-исполнителя	182	180	99	219 020 391	205 677 619	13 342 772	94
Индивидуальный проект по ХФУ	449	449	100	18 859 831	18 859 831	0	100
Планы поэтапного отказа от ХФУ	117	117	100	9 549 588	9 549 588	1	100
Удаление	2	2	100	190 040	190 040	0	100
Энергоэффективность	6	0	0	1 617 200	109 657	1 507 543	7
Правительственная поддержка	1 063	968	91	100 834 251	86 022 781	14 811 470	85
Индивидуальный проект по ГХФУ	312	278	89	12 780 387	11 705 070	1 075 316	92
План организационной деятельности по поэтапному отказу от ГХФУ (ПОДПО) (первый этап)	357	345	97	27 708 270	26 507 764	1 200 506	96
ПОДПО, второй этап	225	80	36	44 754 010	22 344 233	22 409 777	50
ПОДПО, третий этап	16	2	12	4 861 825	837 463	4 024 362	17
Индивидуальный проект по ГФУ	316	220	70	26 753 474	19 552 176	7 201 298	73
Кигалийский план регулирования ГФУ (КПР) (этап I)	66	2	3	4 649 415	731 208	3 918 207	16
Прочие индивидуальные проекты по ОРВ	90	90	100	6 781 350	6 781 350	0	100
Прочие секторальные планы по ОРВ	32	32	100	3 527 163	3 527 163	0	100
Итого	**3 233**	**2 765**	**86**	**481 887 196**	**412 395 943**	**69 491 253**	**86**

* За исключением отмененных и переданных проектов.

** За исключением вспомогательных расходов учреждения-исполнителя.

7. Ниже представлены реализация проектов и мероприятий ЮНЕП на 2025 год и совокупно с 1991 года по 31 декабря 2025 года:

a) **поэтапный отказ**[6]**:** в 2025 году было поэтапно сокращено потребление ОРВ на 19,8 тонн ОРС, а потребление ГФУ — на 28,2 т (48 165 тонн CO_2-экв.), а также был утвержден поэтапный отказ от потребления ОРВ в дополнительном объеме 33,6 тонн ОРС, а ГФУ — в объеме 162,2 т (380 774 тонны CO_2-экв.). С 1991 года было поэтапно сокращено потребление ОРВ в объеме 2 283 тонны ОРС от ожидаемого общего потребления ОРВ в объеме 2 719 тонн ОРС, а потребление ГФУ — в объеме 36 т (68 058 тонн CO_2-экв.) от ожидаемого общего объема потребления ГФУ в 873 т (1 826 294 тонны CO_2-экв.) по утвержденным проектам (за исключением отмененных и переданных проектов);

b) **выплаты/утвержденные средства:** в 2025 году было выплачено 23,2 млн долл. США, а на основе отчета о ходе работы за 2024 год было

[6] Поэтапный отказ от ОРВ выражается в тоннах ОРС, а от ГФУ — в т и тоннах CO_2-экв.

запланировано выплатить 27,2 млн долл. США, что соответствует коэффициенту выплат в 85 процентов от запланированного. В совокупности из общей суммы 481,89 млн долл. США, утвержденной для выплаты (без учета вспомогательных расходов учреждения-исполнителя), было выплачено 412,4 млн долл. США, что соответствует коэффициенту выплат в 86 процентов. В 2025 году для реализации было утверждено 24,05 млн долл. США;

c) **число завершенных проектов:** в 2025 году было завершено 70 проектов. С 1991 года из 3 233 утвержденных проектов (за исключением закрытых или переданных проектов) было завершено 2 765 проектов, что соответствует коэффициенту завершения в 86 процентов;

d) **скорость реализации — неинвестиционные проекты:** проекты, завершенные в 2025 году, были завершены в среднем через 36 месяцев после их утверждения. С 1991 года средний срок реализации неинвестиционных проектов составлял 37 месяцев после их утверждения. Первые выплаты по этим проектам производились в среднем через 12 месяцев после их утверждения;

e) **подготовка проектов:** из 493 мероприятий по подготовке проектов, утвержденных к концу 2025 года, 392 были завершены, 101 мероприятие продолжается. В 2025 году было завершено 19 мероприятий по подготовке проектов;

f) **задержки в реализации:** на конец 2025 года на этапе реализации находилось в общей сложности 468 проектов, которые в среднем имели задержку в семь месяцев. Двадцать семь из этих проектов классифицированы как «проекты с задержками в реализации»[7], и к ним применимы процедуры отмены проекта (к демонстрационным проектам, подготовке проектов и ИС эти процедуры неприменимы); и

g) **многолетние соглашения (МЛС):** в 2025 году в процессе осуществления находилось 95 МЛС по ПОДПО и 57 МЛС по КПР. С 1991 года было утверждено 327 МЛС и завершено 175 МЛС, что соответствует коэффициенту завершения в 54 процента.

8. В таблице 3 приведена краткая информация о ходе работы ЮНЕП с 1991 года.

Таблица 3. Ход работы ЮНЕП с 1991 года

Достигнутый поэтапный отказ		Выплаты (в долл. США)	Количество проектов		Скорость завершения неинвестиционных проектов (в мес.)	Средняя задержка по проектам (в мес.)	Количество МЛС	
тонны ОРС*	тонны CO_2-экв**		Утверждено	Завершено			Утверждено	Завершено
2 283	68 058	412 395 943	3 233	2 765	37	7	327	175

*Потребление ОРВ.
** Связанные с ГФУ проекты.

Связанные с ГФУ проекты

9. По состоянию на 31 декабря 2025 года Исполнительный комитет утвердил 382 проекта, связанных с ГФУ (в том числе 134 подготовительных мероприятия, 182 проекта по оказанию технического содействия и 66 проектов, связанных с этапом I КПР) на общую сумму

[7] Проекты, утвержденные более 18 месяцев назад, с выплатами менее 1% или проекты, не завершенные через 12 месяцев после предложенной даты завершения в отчете о ходе работы (решение 22/61).

31 402 889 долл. США (без учета вспомогательных расходов учреждения-исполнителя). Краткая информация о статусе реализации этих проектов представлена в таблице 4, а соответствующие данные уже включены в пункты 4–8.

Таблица 4. Утвержденные проекты, связанные с ГФУ*

Тип	Количество проектов			Финансирование (в долл. США)**			
	Утверждено	Завершено	% завершения	Утверждено	Выплачено	Баланс	% выплат
Индивидуальные проекты, связанные с ГФУ — подготовительные проекты	134	43	32	11 992 129	5 584 902	6 407 227	47
Индивидуальные проекты, связанные с ГФУ — техническое содействие	182	177	97	14 761 345	13 967 275	794 071	95
Этап I КПР***	66	2	3	4 649 415	731 208	3 918 207	16
Итого	**382**	**222**	**58**	**31 402 889**	**20 283 384**	**11 119 505**	**65**

* За исключением отмененных и переданных проектов.
** За исключением вспомогательных расходов учреждения-исполнителя.
** Был утвержден поэтапный отказ от 873 т (1 826 294 тонн CO_2-экв.) ГФУ.

10. По состоянию на конец 2025 года из 382 проектов было завершено 43 подготовительных мероприятия, 177 проектов по оказанию технического содействия и два проекта, связанных с этапом I КПР, при этом осталось 160 реализуемых проектов. Реализуемые проекты находятся на различных этапах осуществления.

11. Из общей суммы утвержденного финансирования в размере 31 402 889 долл. США (без учета вспомогательных расходов учреждения-исполнителя) было выплачено 20 283 384 долл. США, что составляет 65 процентов от общей суммы.

Проекты в области энергоэффективности

12. По состоянию на 31 декабря 2025 года Исполнительный комитет утвердил шесть проектов в области энергоэффективности (включая пять экспериментальных проектов по оказанию технического содействия в рамках механизма финансирования в соответствии с решением 91/65 и один проект по оказанию технического содействия «Координирование работы национальных должностных лиц по озоновому слою и национальных политиков, занимающихся вопросами энергоэффективности, в поддержку Кигалийской поправки») на сумму 1 617 200 долл. США (без учета вспомогательных расходов учреждения-исполнителя). Краткая информация о статусе реализации этих проектов представлена в таблице 5, а соответствующие данные уже включены в пункты 4–8.

Таблица 5. Утвержденные проекты в области энергоэффективности*

Тип	Количество проектов			Финансирование (в долл. США)**			
	Утверждено	Завершено	% завершения	Утверждено	Выплачено	Баланс	% выплат
Экспериментальные проекты (решение 91/65) — техническое содействие	5	0	0	824 000	109 657	714 343	13
Прочее техническое содействие	1	0	0	793 200	0	793 200	0
Итого	**6**	**0**	**0**	**1 617 200**	**109 657**	**1 507 543**	**7**

* За исключением отмененных проектов.

** За исключением вспомогательных расходов учреждения-исполнителя.

13. По состоянию на конец 2025 года все утвержденные проекты находились в процессе реализации. Из общей суммы утвержденного финансирования в размере 1 617 200 долл. США (без учета вспомогательных расходов учреждения-исполнителя) было выплачено 109 657 долл. США, что составляет 7 процентов от общей суммы.

Проблемы, выявленные при реализации проектов в 2025 году

14. По итогам процесса обзора было обсуждено и удовлетворительным образом урегулировано несколько вопросов за исключением вопросов, касающихся 27 проектов, классифицированных как проекты с задержками в реализации (в том числе 26 проектов, связанных с компонентами МЛС, в отношении которых применимы процедуры отмены проекта в соответствии с решением 84/45 c); и один проект по оказанию технического содействия). В приложении III к настоящему документу представлены проекты с задержками в реализации, а также рекомендации Секретариата с поручением представить отчет 100-му совещанию.

15. Кроме того, были выявлены проблемы, связанные с проектами или траншами МЛС для поэтапного-отказа от ГХФУ и ГФУ; возобновлением проектов по ИС; подготовкой ПОДПО; проектами, утвержденными решением 91/66; и созданием условий для поэтапного сокращения ГФУ. Эти проблемы также представлены в приложении III. По каждому из этих проектов представлена краткая информация о статусе реализации и неурегулированных вопросах, а также предложена рекомендация для рассмотрения Исполнительным комитетом.

16. Подробная информация о ходе реализации связанных с ПОДПО проектов Барбадоса[8], Китая (обслуживание)[9], Сальвадора[10], Эфиопии[11], Габона[12], Гренады[13], Индии[14], Ирака[15], Монголии[16], Мозамбика[17], Катара[18], Сан-Томе и Принсипи[19], Саудовской Аравии[20], Сербии[21], Сьерра-Леоне[22],

[8] UNEP/OzL.Pro/ExCom/99/39
[9] UNEP/OzL.Pro/ExCom/99/45
[10] UNEP/OzL.Pro/ExCom/99/51
[11] UNEP/OzL.Pro/ExCom/99/52
[12] UNEP/OzL.Pro/ExCom/99/53
[13] UNEP/OzL.Pro/ExCom/99/54
[14] UNEP/OzL.Pro/ExCom/99/56
[15] UNEP/OzL.Pro/ExCom/99/57
[16] UNEP/OzL.Pro/ExCom/99/61
[17] UNEP/OzL.Pro/ExCom/99/62
[18] UNEP/OzL.Pro/ExCom/99/68
[19] UNEP/OzL.Pro/ExCom/99/69
[20] UNEP/OzL.Pro/ExCom/99/70
[21] UNEP/OzL.Pro/ExCom/99/71
[22] UNEP/OzL.Pro/ExCom/99/72

Шри-Ланки[23], Тимора-Лешти[24] и Объединенной Республики Танзании[25], с КПР Камбоджи[26], Конго[27], Доминиканской Республики[28] и Кыргызстана[29], а также отчеты о проектах с конкретными требованиями к представлению отчетности[30], связанных с Бангладеш (ПОДПО) и Сенегалом (ПОДПО), представлены 99-му совещанию. Рекомендации по неурегулированным вопросам в отношении этих проектов, включая утверждение запросов о продлении сроков, если таковые имеются, рассматриваются в соответствующих разделах этих документов. Неурегулированные вопросы в отношении остальных реализуемых проектов, не включенных в приложение III к настоящему документу, и запросы о продлении сроков завершения рассматриваются ниже.

17. Из 272 реализуемых проектов, за исключением проектов по ИС и подготовки проектов, по 63 проектам с момента представления отчета о ходе работы за 2024 год пересмотрены запланированные сроки завершения.

18. В соответствии с решением 95/12 b), Секретариат отметил, что в течение последних трех лет не поступало запросов о возобновлении проектов по ИС в трех странах, действующих в рамках статьи 5, а именно: Алжире, Мьянме и Науру. Основными причинами непредставления запросов были административные трудности и институциональные проблемы, политическая нестабильность и ситуация в области безопасности, а также значительные остатки средств от ранее утвержденных этапов проектов по ИС. ЮНЕП сообщила, что она активно поддерживает эти страны и планирует представить запросы о возобновлении к 2027 году, за исключением Мьянмы, где подача запроса зависит от политической ситуации в стране и возобновления мероприятий.

19. В соответствии с решением 82/11 b)[31], ЮНЕП запросила продление срока реализации 35 проектов, утвержденных решением 91/66, как представлено в таблице 6.

Таблица 6. Проекты, по которым, в соответствии с решением 91/66, было запрошено продление срока завершения

Страновой / проектный код	Выплаты (%)	Мероприятия, требующие дополнительного времени	Изначальный срок завершения (мм-гг)	Запрашиваемый срок завершения (мм-гг)
Подготовка национального кадастра запасов отходов регулируемых веществ и разработка национального плана управления этими веществами (решение 91/66)				
Багамские Острова BHS/HFCIND/38/UNEP/PRP/DES/95	8	Завершение подготовки кадастра и плана действий	дек-26	июнь-27
Бутан BTN/HFCIND/37/UNEP/PRP/DES/95	0	Завершение обследования и остальных мероприятий, а также подготовки отчета	дек-26	дек-27
Бруней-Даруссалам BRN/HFCIND/35/UNEP/PRP/DES/95	1	Завершение сбора данных, оценка условий регулирования окончания жизненного цикла в консультации с соответствующими	дек-26	дек-27

[23] UNEP/OzL.Pro/ExCom/99/73
[24] UNEP/OzL.Pro/ExCom/99/74
[25] UNEP/OzL.Pro/ExCom/99/76
[26] UNEP/OzL.Pro/ExCom/99/43
[27] UNEP/OzL.Pro/ExCom/99/47
[28] UNEP/OzL.Pro/ExCom/99/50
[29] UNEP/OzL.Pro/ExCom/99/58
[30] UNEP/OzL.Pro/ExCom/99/19 или UNEP/OzL.Pro/ExCom/99/20
[31] Любой запрос о продлении срока должен быть представлен на утверждение Исполнительному комитету до даты завершения проекта, принимая во внимание, что новые обязательства до утверждения продления возникать не должны.

Страновой / проектный код	Выплаты (%)	Мероприятия, требующие дополнительного времени	Изначальный срок завершения (мм-гг)	Запрашиваемый срок завершения (мм-гг)
		заинтересованными сторонами и завершение подготовки рекомендаций по политическим стратегиям и плану действий		
Острова Кука COK/HFCIND/23/UNEP/PRP/DES/95	0	Завершение оценки условий и разработка рекомендаций по политическим стратегиям и планов действий в консультации с Центром международного сотрудничества в целях экооценки (ОЕКК), Японией и соответствующими заинтересованными сторонами в целях обеспечения соответствия в контексте страны	дек-26	дек-27
Фиджи FJI/HFCIND/47/UNEP/PRP/DES/95	0			
Кирибати KIR/HFCIND/23/UNEP/PRP/DES/95	0			
Маршалловы Острова MHL/HFCIND/23/UNEP/PRP/DES/95	0			
Микронезия (Федеративные Штаты) FSM/HFCIND/22/UNEP/PRP/DES/95	0			
Науру NRU/HFCIND/19/UNEP/PRP/DES/95	0			
Ниуэ NIU/HFCIND/22/UNEP/PRP/DES/95	0			
Палау PLW/HFCIND/24/UNEP/PRP/DES/95	0			
Самоа WSM/HFCIND/32/UNEP/PRP/DES/95	0		дек-26	дек-27
Соломоновы Острова SLB/HFCIND/25/UNEP/PRP/DES/95	43		дек-26	дек-27
Тонга TON/HFCIND/24/UNEP/PRP/DES/95	0		дек-26	дек-27
Тувалу TUV/HFCIND/23/UNEP/PRP/DES/95	0		дек-26	дек-27
Вануату VUT/HFCIND/23/UNEP/PRP/DES/95	0		дек-26	дек-27
Регион: Азия и Тихий океан ASP/HFCIND/72/UNEP/PRP/DES/95	0	Завершение оценки условий и разработка рекомендаций по политическим стратегиям и планов действий в консультации с ОЕКК, Японией и соответствующими заинтересованными сторонами в целях обеспечения соответствия в контексте страны, а также организация регионального рабочего совещания	дек-26	дек-27
Эритрея ERI/HFCIND/31/UNEP/PRP/DES/94	78	Завершение сбора и анализа данных, а также подготовки отчета	июнь-26	июнь-27
Эсватини SWZ/HFCIND/43/UNEP/PRP/DES/95	0	Завершение сбора и анализа данных, а также подготовки отчета	дек-26	июнь-27
Гамбия GMB/HFCIND/55/UNEP/PRP/DES/95	0	Завершение сбора и анализа данных, а также подготовки отчета	дек-26	июнь-27

Страновой / проектный код	Выплаты (%)	Мероприятия, требующие дополнительного времени	Изначальный срок завершения (мм-гг)	Запрашиваемый срок завершения (мм-гг)
Кыргызстан KGZ/HFCIND/54/UNEP/PRP/DES/94	80	Завершение сбора и анализа данных, а также подготовки отчета	июнь-26	дек-26
Лаосская Народно-Демократическая Республика LAO/HFCIND/47/UNEP/PRP/DES/94	24	Завершение подготовки национального кадастрового отчета, оценка вариантов условий в консультации с соответствующими заинтересованными сторонами и разработка рекомендаций по политическим стратегиям и планов действий	июнь-26	июнь-27
Лесото LSO/HFCIND/37/UNEP/PRP/DES/94	50	Завершение сбора и анализа данных, а также подготовки отчета	июнь-26	июнь-27
Малави MWI/HFCIND/61/UNEP/PRP/DES/94	97	Завершение внутренней проверки, а также подготовки отчета	июнь-26	дек-26
Мальдивские Острова MDV/HFCIND/43/UNEP/PRP/DES/95	0	Завершение анализа планируемых мероприятий, а также подготовки отчета	дек-26	дек-27
Монголия MNG/HFCIND/43/UNEP/PRP/DES/95	0	Завершение сбора и анализа данных, а также подготовки отчета	дек-26	дек-27
Непал NPL/HFCIND/50/UNEP/PRP/DES/95	0	Завершение сбора и анализа данных, а также подготовки отчета	дек-26	дек-27
Нигерия NGA/HFCIND/171/UNEP/PRP/DES/94	40	Завершение внутренней проверки, а также подготовки отчета	июнь-26	дек-26
Сьерра-Леоне SLE/HFCIND/53/UNEP/PRP/DES/94	0	Завершение внутренней проверки, а также подготовки отчета	май-26	дек-26
Шри-Ланка LKA/HFCIND/70/UNEP/PRP/DES/95	0	Завершение обследования и остальных мероприятий, а также подготовки отчета	дек-26	дек-27
Тимор-Лешти TLS/HFCIND/32/UNEP/PRP/DES/95	0	Завершение сбора данных, оценка вариантов условий в консультации с соответствующими заинтересованными сторонами и разработка рекомендаций по политическим стратегиям и планов действий	дек-26	дек-27
Уганда UGA/HFCIND/42/UNEP/PRP/DES/95	0	Завершение обследования, а также подготовки отчета	дек-26	июнь-27
Йемен YEM/HFCIND/49/UNEP/PRP/DES/93	13	Адаптация рабочих процессов на местах и осуществление протоколов обеспечения безопасности в ответ на текущую ситуацию в области безопасности; завершение	дек-25*	дек-27

Страновой / проектный код	Выплаты (%)	Мероприятия, требующие дополнительного времени	Изначальный срок завершения (мм-гг)	Запрашиваемый срок завершения (мм-гг)
		сбора требуемых данных, насколько позволяют условия; и завершение подготовки доклада		
Замбия ZMB/HFCIND/50/UNEP/PRP/DES/94	0	Завершение мероприятий по проведению обследования, а также подготовки отчета	июнь-26	июнь-27
Зимбабве ZWE/HFCIND/74/UNEP/PRP/DES/94	49	Завершение мероприятий по проведению обследования, а также подготовки отчета	июнь-26	июнь-27

* Дата завершения уже была перенесена на июнь 2026 года (решение 97/12 b) i)).

Учет гендерной проблематики[32]

20. Все проекты ЮНЕП регулируются внутренним планом подразделения «ОзонЭкшн» и основной группой, поддерживающей региональные группы Программы содействия соблюдению по вопросам участия и расширения экономических прав и возможностей женщин; они согласуются с политикой Многостороннего фонда в этой области. Подразделение ЮНЕП «ОзонЭкшн» тесно сотрудничает с правительствами и другими соответствующими заинтересованными сторонами для того, чтобы соображения, касающиеся участия и представительства женщин, эффективно учитывались при разработке и осуществлении проектов. ЮНЕП провела анализ 33 этапов I КПР, представленных в период с 2023 по 2026 год, для которых ЮНЕП является ведущим учреждением-исполнителем. Анализ показывает, что все 33 проекта включают мероприятия и показатели, способствующие участию и представленности женщин; 20 — имеют специальные бюджеты для проведения соответствующих мероприятий; 24 проекта способствуют участию женщин в учебных программах по холодильному оборудованию и системам кондиционирования воздуха; 16 — способствуют участию женщин в обучении таможенных и правоохранительных органов; 26 — обеспечивают сбор данных с разбивкой по полу; и 12 — привлекают женские организации или специалистов в этой области. Кроме того, ЮНЕП тесно сотрудничает с правительствами в целях осуществления конкретных корректировок или обновления деятельности по проектам для повышения эффективности осуществления соответствующих политических стратегий на национальном уровне.

Управление рисками

21. ЮНЕП располагает системой систематического мониторинга рисков для партнеров-исполнителей, внедренной в ответ на рекомендацию Комиссии ревизоров ООН (A/80/5/Add.7, пункт 70) и проблем, выявляемых в ходе реализации проектов в различных странах и регионах. Автоматизированные проверки, основанные на принципе «красного флажка», запускают подготовку финансовых и ревизионных отчетов по случаям просрочек, несоблюдению правовых положений, неблагоприятных отклонений в бюджете, неурегулированных неприемлемых расходов и негативных результатов ревизий, проводимую на ранних этапах цикла партнерских отношений. Для обеспечения надлежащего устранения задержек в реализации проектов ЮНЕП проводит регулярные мероприятия с национальными органами по озоновому слою, корректирует планы работы и сроки, проводит встречи на уровне руководства для обеспечения участия правительств на высоком уровне, содействует проведению координационных совещаний заинтересованных сторон

[32] Исполнительный комитет поручил двусторонним учреждениям и учреждениям-исполнителям с 2023 года представлять краткую информацию о ключевых результатах в области учета гендерной проблематики в рамках их ежегодных отчетов о ходе работы на основе имеющейся у них информации (решение 90/48 d)).

и разрабатывает дорожные карты осуществления. В случае необходимости для обеспечения участия правительства на самом высоком уровне запрашивается поддержка со стороны высшего руководства.

Рекомендация

22. Исполнительный комитет может посчитать целесообразным:

a) принять к сведению отчет о ходе работы ЮНЕП по состоянию на 31 декабря 2025 года, содержащийся в документе UNEP/OzL.Pro/ExCom/99/16;

b) утвердить продление сроков завершения подготовки национальных кадастров запасов отходов регулируемых веществ и разработки национальных планов для управления этими веществами (решение 91/66) для перечисленных ниже стран, с тем чтобы они смогли завершить оставшиеся реализуемые мероприятия, как отражено в таблице 6 документа UNEP/OzL.Pro/ExCom/99/16:

i) до декабря 2026 года:

a. Кыргызстан (KGZ/HFCIND/54/UNEP/PRP/DES/94);

b. Малави (MWI/HFCIND/61/UNEP/PRP/DES/94);

c. Нигерия (NGA/HFCIND/171/UNEP/PRP/DES/94);

d. Сьерра-Леоне (SLE/HFCIND/53/UNEP/PRP/DES/94);

ii) до июня 2027 года:

a. Багамские Острова (BHS/HFCIND/38/UNEP/PRP/DES/95);

b. Эритрея (ERI/HFCIND/31/UNEP/PRP/DES/94);

c. Эсватини (SWZ/HFCIND/43/UNEP/PRP/DES/95);

d. Гамбия (GMB/HFCIND/55/UNEP/PRP/DES/95);

e. Лаосская Народно-Демократическая Республика (LAO/HFCIND/47/UNEP/PRP/DES/94);

f. Лесото (LSO/HFCIND/37/UNEP/PRP/DES/94);

g. Уганда (UGA/HFCIND/42/UNEP/PRP/DES/95);

h. Замбия (ZMB/HFCIND/50/UNEP/PRP/DES/94);

i. Зимбабве (ZWE/HFCIND/74/UNEP/PRP/DES/94);

iii) до декабря 2027 года:

a. Бутан (BTN/HFCIND/37/UNEP/PRP/DES/95);

b. Бруней-Даруссалам (BRN/HFCIND/35/UNEP/PRP/DES/95);

c. Острова Кука (COK/HFCIND/23/UNEP/PRP/DES/95);

d. Фиджи (FJI/HFCIND/47/UNEP/PRP/DES/95);

e. Кирибати (KIR/HFCIND/23/UNEP/PRP/DES/95);

f. Мальдивские Острова (MDV/HFCIND/43/UNEP/PRP/DES/95);

g. Маршалловы Острова (MHL/HFCIND/23/UNEP/PRP/DES/95);

h. Микронезия (Федеративные Штаты) (FSM/HFCIND/22/UNEP/PRP/DES/95);

i. Монголия (MNG/HFCIND/43/UNEP/PRP/DES/95);

j. Науру (NRU/HFCIND/19/UNEP/PRP/DES/95);

k. Непал (NPL/HFCIND/50/UNEP/PRP/DES/95);

l. Ниуэ (NIU/HFCIND/22/UNEP/PRP/DES/95);

m. Палау (PLW/HFCIND/24/UNEP/PRP/DES/95);

n. Самоа (WSM/HFCIND/32/UNEP/PRP/DES/95);

o. Соломоновы Острова (SLB/HFCIND/25/UNEP/PRP/DES/95);

p. Шри-Ланка (LKA/HFCIND/70/UNEP/PRP/DES/95);

q. Тимор-Лешти (TLS/HFCIND/32/UNEP/PRP/DES/95);

r. Тонга (TON/HFCIND/24/UNEP/PRP/DES/95);

s. Тувалу (TUV/HFCIND/23/UNEP/PRP/DES/95);

t. Вануату (VUT/HFCIND/23/UNEP/PRP/DES/95);

u. Йемен (YEM/HFCIND/49/UNEP/PRP/DES/93);

v. Регион: Азия и Тихий океан (ASP/HFCIND/72/UNEP/PRP/DES/95); и

c) утвердить также рекомендации, касающиеся реализуемых проектов с конкретными вопросами, как представлено в приложении III к настоящему документу.

Приложение I

ОБЗОР СТАТУСА РЕАЛИЗАЦИИ ПРОЕКТОВ ЮНЕП ПО СТРАНАМ НА 2025 ГОД

1. В таблице 1 приложения I представлена информация о статусе реализации проектов по странам на 2025 год в разбивке по достигнутому уровню поэтапного отказа, запланированным и осуществленным выплатам и завершению проектов.

Таблица 1. Статус реализации проектов ЮНЕП на 2025 год

Страна	Поэтапный отказ в 2025 году (тонны ОРС)	Поэтапный отказ в 2025 году (тонны CO2-экв.)*	Оценочный объем выплат в 2025 году (в долл. США)	Выплата средств в 2025 году (в долл. США)	Процент выплаты средств в 2025 году в сравнении с оценкой	Процент запланированных проектов, завершенных в 2025 году**
Албания	0,6	0	37 980	100 283	264	100
Алжир	0,0	0	142 236	90 000	63	
Ангола	0,0	0	19 912	126 852	637	100
Антигуа и Барбуда	0,0	0	48 927	33 944	69	
Армения	0,0	0	44 287	29	0	0
Багамские Острова	0,0	0	83 400	57 049	68	
Бахрейн	2,0	0	53 042	158 008	298	
Бангладеш	0,0	0	249 909	170 061	68	0
Барбадос	0,0	0	106 940	16 502	15	
Белиз	0,0	0	127 212	64 060	50	100
Бенин	0,0	0	74 458	64 827	87	0
Бутан	0,0	0	115 801	88 037	76	100
Боливия (Многонациональное Государство)	0,0	0	89 242	28 080	31	
Ботсвана	0,0	0	36 570	9 611	26	
Бруней-Даруссалам	0,0	0	142 492	104 330	73	100
Буркина-Фасо	0,0	0	49 607	148 429	299	0
Бурунди	0,0	0	86 150	74 390	86	
Кабо-Верде	0,0	0	185 768	130 484	70	100
Камбоджа	4,9	0	180 388	271 822	151	100
Камерун	0,0	0	92 426	92 450	100	
Центральноафриканская Республика	0,0	0	18 000	72 000	400	
Чад	0,0	0	66 600	201 245	302	
Чили	0,0	0	117 325	74 120	63	
Китай	0,0	0	1 857 230	1 783 754	96	100
Коморские Острова	0,0	0	131 003	3 179	2	
Конго	0,0	0	89 101	19 863	22	
Острова Кука	0,0	0	249 142	87 053	35	0
Коста-Рика	0,0	0	21 485	1 515	7	
Кот-д'Ивуар	0,0	0	291 328	256 193	88	
Демократическая Республика Конго	0,0	0	97 356	105 157	108	
Джибути	0,0	0	86 670	141 715	164	100
Доминика	0,0	0	53 645	34 257	64	
Доминиканская Республика	0,0	0	151 120	143 391	95	
Египет	0,0	0	56 000	164 738	294	
Сальвадор	0,0	0	53 741	37 613	70	100
Экваториальная Гвинея	0,0	0	79 340	62 400	79	
Эритрея	0,0	0	63 242	213 125	337	100

Страна	Поэтапный отказ в 2025 году (тонны ОРС)	Поэтапный отказ в 2025 году (тонны CO2-экв.)*	Оценочный объем выплат в 2025 году (в долл. США)	Выплата средств в 2025 году (в долл. США)	Процент выплаты средств в 2025 году в сравнении с оценкой	Процент запланированных проектов, завершенных в 2025 году**
Эсватини	0,0	0	101 275	122 825	121	
Эфиопия	0,0	0	23 386	46 486	199	100
Фиджи	0,0	0	139 586	116 049	83	33
Габон	0,0	0	122 327	181 225	148	
Гамбия	0,0	0	99 288	200 265	202	
Грузия	0,0	0	20 500	82 000	400	100
Гана	0,0	0	29 932	0	0	
Гренада	0,0	0	172 375	167 486	97	
Гватемала	0,0	0	155 820	51 767	33	100
Гвинея	0,0	0	51 300	122 042	238	100
Гвинея-Бисау	0,0	0	122 423	210 666	172	100
Гайана	0,1	0	83 875	53 948	64	
Гондурас	0,0	0	71 253	48 694	68	100
Индия	0,0	0	536 672	345 133	64	
Иран (Исламская Республика)	0,0	0	159 300	90 956	57	0
Ирак	0,0	0	217 476	120 008	55	
Ямайка	0,0	0	36 545	31 437	86	
Кения	0,0	0	93 475	196 773	211	0
Кирибати	0,0	0	263 592	31 806	12	0
Кувейт	0,0	0	556 899	27 085	5	
Кыргызстан	0,0	0	114 761	242 769	212	100
Лаосская Народно-Демократическая Республика	0,0	0	119 996	141 958	118	100
Лесото	0,0	0	44 400	143 978	324	
Либерия	0,0	0	68 580	123 003	179	100
Мадагаскар	3,4	0	80 825	171 095	212	100
Малави	2,0	48 165	62 802	291 242	464	
Мальдивские Острова	0,0	0	138 597	106 931	77	100
Мали	0,0	0	81 480	219 996	270	100
Маршалловы Острова	0,0	0	110 710	27 711	25	50
Мавритания	0,0	0	31 750	13 750	43	
Маврикий	0,0	0	45 000	0	0	
Мексика	0,0	0	56 949	87 724	154	
Микронезия (Федеративные Штаты)	0,0	0	236 884	59 294	25	0
Монголия	0,0	0	148 679	144 597	97	50
Марокко	0,0	0	103 335	0	0	
Мозамбик	0,0	0	128 534	152 762	119	
Мьянма	0,0	0	45 000	0	0	0
Намибия	0,0	0	68 425	68 425	100	100
Науру	0,0	0	151 660	5 766	4	0
Непал	0,0	0	123 057	12 681	10	100
Никарагуа	0,0	0	185 932	94 458	51	
Нигер	1,7	0	73 500	48 199	66	100
Нигерия	0,0	0	38 080	40 400	106	
Ниуэ	0,0	0	68 475	34 574	50	0
Оман	0,0	0	78 829	163 207	207	
Пакистан	0,0	0	295 048	148 700	50	
Палау	0,0	0	218 775	75 250	34	0
Парагвай	0,0	0	114 870	133 845	117	
Перу	2,2	0	138 018	116 356	84	

Страна	Поэтапный отказ в 2025 году (тонны ОРС)	Поэтапный отказ в 2025 году (тонны CO2-экв.)*	Оценочный объем выплат в 2025 году (в долл. США)	Выплата средств в 2025 году (в долл. США)	Процент выплаты средств в 2025 году в сравнении с оценкой	Процент запланированных проектов, завершенных в 2025 году**
Филиппины	0,0	0	99 243	155 439	157	
Катар	0,0	0	95 079	73 187	77	
Республика Молдова	0,0	0	77 280	167 991	217	50
Руанда	0,0	0	49 040	90 916	185	
Сент-Китс и Невис	0,0	0	25 500	14 372	56	
Сент-Люсия	0,0	0	160 000	19 554	12	
Сент-Винсент и Гренадины	0,0	0	149 754	40 069	27	100
Самоа	0,0	0	202 514	55 568	27	0
Сан-Томе и Принсипи	0,0	0	137 086	10 005	7	
Саудовская Аравия	0,0	0	535 786	148 047	28	
Сенегал	0,0	0	217 289	266 384	123	0
Сербия	0,0	0	32 572	20 642	63	0
Сейшельские Острова	0,0	0	34 209	16 488	48	
Сьерра-Леоне	0,1	0	126 609	75 804	60	
Соломоновы Острова	0,0	0	287 567	120 792	42	0
Сомали	0,0	0	79 950	105 209	132	
Южный Судан	0,0	0	50 000	110 310	221	100
Шри-Ланка	0,0	0	107 781	48 780	45	100
Суринам	0,0	0	135 391	68 710	51	100
Сирийская Арабская Республика	0,0	0	310 659	29 939	10	0
Тимор-Лешти	0,0	0	108 121	38 547	36	0
Того	0,0	0	89 460	296 404	331	
Тонга	0,0	0	196 734	115 817	59	0
Тунис	2,8	0	37 500	100 000	267	100
Тувалу	0,0	0	123 680	78 347	63	0
Уганда	0,0	0	43 000	0	0	
Объединенная Республика Танзания	0,0	0	46 210	119 704	259	50
Вануату	0,0	0	249 372	78 797	32	0
Вьетнам	0,0	0	171 632	48 472	28	100
Йемен	0,0	0	137 006	115 022	84	
Замбия	0,0	0	97 350	3 203	3	100
Зимбабве	0,0	0	131 770	210 714	160	
Регион: Азия и Тихий океан	0,0	0	402 457	95 352	24	
Глобально	0,0	0	10 805 809	9 922 172	92	50
Общий итог	**19,8**	**48 165**	**27 232 735**	**23 206 647**	**85**	**59**

* 28,2 т (48 165 тонн CO_2-экв.) в 2025 году по связанным с ГФУ проектам.

** Для проектов, завершение которых было запланировано на 2025 год.

Приложение II

ОБЗОР СТАТУСА РЕАЛИЗАЦИИ ПРОЕКТОВ ЮНЕП ПО ГОДАМ НА 31 ДЕКАБРЯ 2025 ГОДА

1. В таблице 1 приложения II представлен обзор статуса реализации проектов по годам.[1] Все проекты и мероприятия, утвержденные с 1991 по 2017 год, к настоящему времени завершены.

Таблица 1. Статус реализации проектов по годам*

Год	Количество проектов			Финансирование (в долл. США)**			
	Утверждено	Завершено	% завершения	Утверждено	Выплачено	Баланс	% выплат
1991	11	11	100	1 372 335	1 372 335	0	100
1992	15	15	100	1 711 000	1 711 000	0	100
1993	49	49	100	4 194 343	4 194 343	0	100
1994	58	58	100	4 231 169	4 231 169	0	100
1995	50	50	100	4 047 683	4 047 683	0	100
1996	47	47	100	3 345 039	3 345 039	0	100
1997	87	87	100	7 962 291	7 962 291	0	100
1998	64	64	100	4 669 124	4 669 124	0	100
1999	87	87	100	6 368 983	6 368 983	0	100
2000	85	85	100	6 300 398	6 300 398	0	100
2001	59	59	100	7 411 159	7 411 159	0	100
2002	72	72	100	9 469 401	9 469 401	0	100
2003	78	78	100	11 165 394	11 165 394	0	100
2004	99	99	100	12 362 652	12 362 652	0	100
2005	72	72	100	12 339 483	12 339 483	0	100
2006	108	108	100	12 731 484	12 731 484	0	100
2007	79	79	100	14 611 111	14 611 111	0	100
2008	132	132	100	17 875 070	17 875 070	0	100
2009	115	115	100	17 250 876	17 250 876	0	100
2010	79	79	100	14 356 674	14 356 674	0	100
2011	100	100	100	16 782 433	16 782 434	-1	100
2012	80	80	100	16 086 261	16 086 261	0	100
2013	90	90	100	14 152 112	14 152 112	-1	100
2014	74	74	100	12 328 954	12 328 953	1	100
2015	180	180	100	21 169 099	21 169 098	1	100
2016	95	95	100	19 552 807	19 552 805	2	100
2017	88	88	100	15 532 086	15 532 085	1	100
2018	173	172	99	23 738 631	23 651 458	87 173	100
2019	110	107	97	14 871 180	14 784 683	86 496	99
2020	130	107	82	15 165 976	13 179 022	1 986 954	87
2021	126	109	87	21 847 003	20 770 089	1 076 914	95
2022	101	75	74	22 864 789	19 382 170	3 482 619	85
2023	125	36	29	27 139 094	17 048 683	10 090 412	63
2024	213	6	3	42 833 659	13 954 105	28 879 554	33
2025	102	0	0	24 047 446	246 316	23 801 130	1
Итого	**3 233**	**2 765**	**86**	**481 887 196**	**412 395 943**	**69 491 253**	**86**

* За исключением закрытых и переданных проектов.
** За исключением вспомогательных расходов учреждения-исполнителя.

[1] Данные представлены по годам утверждения проектов Исполнительным комитетом. Все утверждения (инвестиционные и неинвестиционные проекты) рассматриваются на равных условиях (т. е. инвестиционный проект или транш финансирования МЛС на 1 млн долл. США считается одним проектом, как и подготовка страновой программы на 30 000 долл. США). Ключевые показатели из годового отчета: процент завершенных проектов, поэтапный отказ от тонн ОРС/тонн CO_2-экв. и процент выплаченных средств. Существует три типа выплат: на этапе реализации, после реализации, а также для проектов, финансируемых задним числом.

Приложение III

РЕАЛИЗУЕМЫЕ ПРОЕКТЫ С НЕУРЕГУЛИРОВАННЫМИ ВОПРОСАМИ В ОТЧЕТЕ О ХОДЕ РАБОТЫ ДЛЯ ЮНЕП

Страна	Проектный код	Наименование проекта	Выплаты (%)	Статус/Проблемы	Рекомендация
Алжир	DZA/HPMP2/88/UNEP/TAS/SRV/95	План организационной деятельности по поэтапному отказу от ГХФУ (второй этап, первый транш)	0	Медленный прогресс в реализации	Поручить ЮНЕП представить 100-му совещанию отчет о ходе реализации и уровне расходования средств
Боливия (Многонациональное Государство)	BOL/HPMP2/56/UNEP/TAS/SRV/93	План организационной деятельности по поэтапному отказу от ГХФУ (второй этап, второй транш)	0	18-месячная задержка	Поручить ЮНЕП представить 100-му совещанию отчет об этом проекте с задержками в реализации
Боливия (Многонациональное Государство)	BOL/HPMP2/61/UNEP/TAS/SRVEE/93	План организационной деятельности по поэтапному отказу от ГХФУ (второй этап) (дополнительные мероприятия по поддержанию энергоэффективности в секторе обслуживания холодильного оборудования (решение 89/6))	0	18-месячная задержка	Поручить ЮНЕП представить 100-му совещанию отчет об этом проекте с задержками в реализации
Коморские Острова	COM/HPMP2/37/UNEP/TAS/SRV/94	План организационной деятельности по поэтапному отказу от ГХФУ (второй этап, первый транш)	0	18-месячная задержка	Поручить ЮНЕП представить 100-му совещанию отчет об этом проекте с задержками в реализации
Демократическая Республика Конго	COD/HCFCIND/52/UNEP/TAS/VER/92	Отчет о проверке реализации второго этапа Плана организационной деятельности по поэтапному отказу от ГХФУ	0	18-месячная задержка	Поручить ЮНЕП представить 100-му совещанию отчет об этом проекте с задержками в реализации
Эсватини	SWZ/HPMP2/39/UNEP/TAS/SRV/94	План организационной деятельности по поэтапному отказу от ГХФУ (второй этап, второй транш)	0	18-месячная задержка	Поручить ЮНЕП представить 100-му совещанию отчет об этом проекте с задержками в реализации

Страна	Проектный код	Наименование проекта	Выплаты (%)	Статус/Проблемы	Рекомендация
Эсватини	SWZ/HPMP2/41/UNEP/TAS/SRVEE/94	План организационной деятельности по поэтапному отказу от ГХФУ (второй этап) (дополнительные мероприятия по поддержанию энергоэффективности в секторе обслуживания холодильного оборудования (решение 89/6))	0	18-месячная задержка	Поручить ЮНЕП представить 100-му совещанию отчет об этом проекте с задержками в реализации
Экваториальная Гвинея	GNQ/HCFCIND/17/UNEP/PRP/SRV/84	Подготовка Плана организационной деятельности по поэтапному отказу от ГХФУ (второй этап)	15	Медленный прогресс в реализации	Поручить ЮНЕП представить 100-му совещанию отчет о статусе представления второго этапа ПОДПО
Гана	GHA/KIP1/59/UNEP/TAS/SRV/93	Кигалийский план регулирования ГФУ (первый этап, первый транш)	0	18-месячная задержка	Поручить ЮНЕП представить 100-му совещанию отчет об этом проекте с задержками в реализации
Гана	GHA/KIP1/60/UNEP/TAS/SRV/93	Кигалийский план регулирования ГФУ (первый этап, первый транш)	0	18-месячная задержка	Поручить ЮНЕП представить 100-му совещанию отчет об этом проекте с задержками в реализации
Гватемала	GTM/HPMP2/64/UNEP/TAS/SRV/93	План организационной деятельности по поэтапному отказу от ГХФУ (второй этап, второй транш)	0	18-месячная задержка	Поручить ЮНЕП представить 100-му совещанию отчет об этом проекте с задержками в реализации
Гондурас	HND/KIP1/65/UNEP/TAS/SRV/94	Кигалийский план регулирования ГФУ (первый этап, первый транш)	0	18-месячная задержка	Поручить ЮНЕП представить 100-му совещанию отчет об этом проекте с задержками в реализации
Иран (Исламская Республика)	IRN/HPMP2/232/UNEP/TAS/SRV/84	План организационной деятельности по поэтапному отказу от ГХФУ (второй этап, второй транш) (сектор	96	12-месячная задержка	Поручить ЮНЕП представить 100-му совещанию отчет об этом проекте с задержками в реализации

Страна	Проектный код	Наименование проекта	Выплаты (%)	Статус/Проблемы	Рекомендация
		обслуживания холодильного оборудования)			
Иран (Исламская Республика)	IRN/HPMP2/246/UNEP/TAS/SRV/86	План организационной деятельности по поэтапному отказу от ГХФУ (второй этап, третий транш) (сектор обслуживания холодильного оборудования)	85	12-месячная задержка	Поручить ЮНЕП представить 100-му совещанию отчет об этом проекте с задержками в реализации
Иран (Исламская Республика)	IRN/HPMP2/272/UNEP/TAS/SRV/94	План организационной деятельности по поэтапному отказу от ГХФУ (второй этап, пятый транш) (сектор обслуживания холодильного оборудования)	0	12- и 18-месячная задержка	Поручить ЮНЕП представить 100-му совещанию отчет об этом проекте с задержками в реализации
Иран (Исламская Республика)	IRN/HPMP3/275/UNEP/TAS/SRV/96	План организационной деятельности по поэтапному отказу от ГХФУ (третий этап, первый транш)	0	Медленный прогресс в реализации	Поручить ЮНЕП представить 100-му совещанию отчет о ходе реализации и уровне расходования средств
Кувейт	KWT/HPMP2/42/UNEP/TAS/SRV/88	План организационной деятельности по поэтапному отказу от ГХФУ (второй этап, первый транш)	47	12-месячная задержка	Поручить ЮНЕП представить 100-му совещанию отчет об этом проекте с задержками в реализации
Мексика	MEX/KIP1/219/UNEP/TAS/PMU/93	Кигалийский план регулирования ГФУ (первый этап, первый транш) (Группа управления проектами)	0	18-месячная задержка	Поручить ЮНЕП представить 100-му совещанию отчет об этом проекте с задержками в реализации
Монголия	MNG/HPMP2/42/UNEP/TAS/SRVEE/93	План организационной деятельности по поэтапному отказу от ГХФУ (второй этап) (дополнительные мероприятия по поддержанию энергоэффективности в секторе обслуживания холодильного оборудования (решение 89/6))	0	18-месячная задержка	Поручить ЮНЕП представить 100-му совещанию отчет об этом проекте с задержками в реализации

Страна	Проектный код	Наименование проекта	Выплаты (%)	Статус/Проблемы	Рекомендация
Мозамбик	MOZ/KIP1/47/UNEP/TAS/SRV/94	Кигалийский план регулирования ГФУ (первый этап, первый транш)	0	18-месячная задержка	Поручить ЮНЕП представить 100-му совещанию отчет об этом проекте с задержками в реализации
Мьянма	MMR/GOV/23/UNEP/INS/NOU/84	Продление проекта по институциональному строительству (этап V: 7/2020-6/2022)	47	Медленный прогресс в реализации	Поручить ЮНЕП представить 100-му совещанию отчет о ходе реализации и уровне расходования средств
Науру	NRU/GOV/16/UNEP/INS/NOU/86	Продление проекта по институциональному строительству (этап VI: 1/2021-12/2022)	7	Медленный прогресс в реализации	Поручить ЮНЕП представить 100-му совещанию отчет о ходе реализации и уровне расходования средств
Науру	NRU/HPMP2/15/UNEP/TAS/SRV/86	План организационной деятельности по поэтапному отказу от ГХФУ для тихоокеанских островных государств с применением регионального подхода (второй этап, первый транш)	15	Медленный прогресс в реализации	Поручить ЮНЕП представить 100-му совещанию отчет о ходе реализации и уровне расходования средств
Науру	NRU/HFCIND/19/UNEP/PRP/DES/95	Подготовка национального кадастра запасов отходов регулируемых веществ и разработка национального плана управления этими веществами (решение 91/66)	0	Медленный прогресс в реализации	Поручить ЮНЕП представить 100-му совещанию отчет о ходе реализации и уровне расходования средств
Науру	NRU/KIP1/20/UNEP/TAS/SRV/95	Кигалийский план регулирования ГФУ (первый этап, первый транш)	0	Медленный прогресс в реализации	Поручить ЮНЕП представить 100-му совещанию отчет о ходе реализации и уровне расходования средств
Науру	NRU/HPMP2/18/UNEP/TAS/SRV/95	План организационной деятельности по поэтапному отказу от ГХФУ (второй этап, второй транш)	0	Медленный прогресс в реализации	Поручить ЮНЕП представить 100-му совещанию отчет о ходе реализации и уровне расходования средств

Страна	Проектный код	Наименование проекта	Выплаты (%)	Статус/Проблемы	Рекомендация
Науру	NRU/HPMP2/21/UNEP/TAS/SRVEE/95	План организационной деятельности по поэтапному отказу от ГХФУ (второй этап) дополнительные мероприятия по поддержанию энергоэффективности в секторе обслуживания холодильного оборудования (решение 89/6)	0	Медленный прогресс в реализации	Поручить ЮНЕП представить 100-му совещанию отчет о ходе реализации и уровне расходования средств
Непал	NPL/HPMP2/43/UNEP/TAS/SRV/86	План организационной деятельности по поэтапному отказу от ГХФУ (второй этап, первый транш)	43	12-месячная задержка	Поручить ЮНЕП представить 100-му совещанию отчет об этом проекте с задержками в реализации
Непал	NPL/GOV/49/UNEP/INS/NOU/95	Продление проекта по институциональному строительству (этап XII: 1/2025-12/2027)	0	Медленный прогресс в реализации	Поручить ЮНЕП представить 100-му совещанию отчет о ходе реализации и уровне расходования средств
Непал	NPL/HPMP2/47/UNEP/TAS/SRV/95	План организационной деятельности по поэтапному отказу от ГХФУ (второй этап, второй транш)	0	12-месячная задержка	Поручить ЮНЕП представить 100-му совещанию отчет об этом проекте с задержками в реализации
Непал	NPL/HFCIND/50/UNEP/PRP/DES/95	Подготовка национального кадастра запасов отходов регулируемых веществ и разработка национального плана управления этими веществами (решение 91/66)	0	Медленный прогресс в реализации	Поручить ЮНЕП представить 100-му совещанию отчет о ходе реализации и уровне расходования средств
Нигер	NER/KIP1/52/UNEP/TAS/SRV/93	Кигалийский план регулирования ГФУ (первый этап)	0	18-месячная задержка	Поручить ЮНЕП представить 100-му совещанию отчет об этом проекте с задержками в реализации
Сент-Люсия	LCA/HPMP2/41/UNEP/TAS/SRV/94	План организационной деятельности по поэтапному отказу от ГХФУ (второй этап, второй транш)	0	18-месячная задержка	Поручить ЮНЕП представить 100-му совещанию отчет об этом

Страна	Проектный код	Наименование проекта	Выплаты (%)	Статус/Проблемы	Рекомендация
					проекте с задержками в реализации
Сент-Люсия	LCA/KIP1/46/UNEP/TAS/SRV/94	Кигалийский план регулирования ГФУ (первый этап, первый транш)	0	18-месячная задержка	Поручить ЮНЕП представить 100-му совещанию отчет об этом проекте с задержками в реализации
Сент-Винсент и Гренадины	VCT/HPMP1/25/UNEP/TAS/SRV/86	План организационной деятельности по поэтапному отказу от ГХФУ (первый этап, третий транш)	31	12-месячная задержка	Поручить ЮНЕП представить 100-му совещанию отчет об этом проекте с задержками в реализации
Сенегал	SEN/HPMP2/48/UNEP/TAS/SRV/88	План организационной деятельности по поэтапному отказу от ГХФУ (второй этап, первый транш)	91	12-месячная задержка	Поручить ЮНЕП представить 100-му совещанию отчет об этом проекте с задержками в реализации
Сьерра-Леоне	SLE/KIP1/54/UNEP/TAS/SRV/94	Кигалийский план регулирования ГФУ (первый этап, первый транш)	0	18-месячная задержка	Поручить ЮНЕП представить 100-му совещанию отчет об этом проекте с задержками в реализации
Сирийская Арабская Республика	SYR/HPMP1/107/UNEP/TAS/SRV/86	План организационной деятельности по поэтапному отказу от ГХФУ (первый этап, первый транш)	75	12-месячная задержка	Поручить ЮНЕП представить 100-му совещанию отчет об этом проекте с задержками в реализации
Йемен	YEM/GOV/48/UNEP/INS/NOU/93	Продление проекта по институциональному строительству (этап IX: 1/2024-12/2026)	23	Медленный прогресс в реализации	Поручить ЮНЕП представить 100-му совещанию отчет о ходе реализации
Йемен	YEM/HFCIND/49/UNEP/PRP/DES/93	Подготовка национального кадастра запасов отходов регулируемых веществ и разработка национального плана управления этими веществами (решение 91/66)	13	Медленный прогресс в реализации	Поручить ЮНЕП представить 100-му совещанию отчет о ходе реализации и уровне расходования средств

Страна	Проектный код	Наименование проекта	Выплаты (%)	Статус/Проблемы	Рекомендация
Йемен	YEM/HFCIND/50/UNEP/TAS/ENA/97	Создание условий для поэтапного сокращения ГФУ	0	Медленный прогресс в реализации	Поручить ЮНЕП представить 100-му совещанию отчет о ходе реализации и уровне расходования средств
Замбия	ZMB/HPMP2/48/UNEP/TAS/SRV/94	План организационной деятельности по поэтапному отказу от ГХФУ (второй этап, второй транш)	0	18-месячная задержка	Поручить ЮНЕП представить 100-му совещанию отчет об этом проекте с задержками в реализации

NARRATIVE OF UNEP 2025 PROGRESS REPORT

Introduction

As of the end of 2025, UNEP was supporting the implementation of Montreal Protocol-related projects in 120 countries, including 87 low-volume-consuming countries (LVCs). The majority of ongoing projects are implemented through National Ozone Units (NOUs), thereby fostering strong national ownership and ensuring the sustainability of project outcomes. UNEP maintains a balanced portfolio across all major project categories, including IS, HPMPs, KIPs, energy efficiency projects under Decisions 89/6 and 91/65, and the preparation of national inventories of banks of waste-controlled substances under Decision 91/66. Consistent with its comparative advantage, UNEP's support is primarily focused on technical assistance and other non-investment activities, with a significant share of its active portfolio concentrated in LVCs.

I. Project summary since the inception of the Multilateral Fund

I.1 Summary data

From June 1991 through December 2025, the Executive Committee approved a total of 3,233 projects for implementation by UNEP, excluding projects that were subsequently closed or transferred. The cumulative value of approvals amounted to US$ $481,887,196, excluding project support costs (PSCs).

During 2025, the Executive Committee approved 102 new projects for UNEP implementation, including the 2026 Compliance Assistance Programme (CAP) budget. The total value of these approvals reached US$24,047,446, with associated project support costs amounting to US$ 2,272,211.

Items	Cumulative since 1991*
Number of Approvals	3,233
Number of completed	2,765
Total funds approved (US$)	481,887,196
Total funds disbursed (US$)	412,395,942
Total approved phase-out (ODP tonnes)**	1,953.6
Total actual phase-out (ODP tonnes)**	2,761.6
Total approved phase-out (metric tonnes)***	873.4
Total actual phase-out (metric tonnes)***	7.7
Total approved phase-out (CO2-eq tonnes)***	1,826,294
Total actual phase-out (CO2-eq tonnes)***	19,893

*Excluding cancelled and transferred projects.

**Including consumption and production.

***For HFC related projects only (including consumption and production).

I.2 Summary data by cluster

The following table summarizes the quantitative summary of UNEP’s project implementation from the Fund’s inception until the end of the reporting period.

Clusters	Number of projects*	Funding (US$)*

	Approved	completed	% completed	Approved	Disbursed	Balance	% disbursed
Agency Programme	182	180	99	219,020,391	205,677,619	13,342,772	94
CFC Individual	449	449	100	18,859,831	18,859,831	0	100
CFC Phase-out Plans	117	117	100	9,549,588	9,549,588	1	100
Disposal	2	2	100	190,040	190,040	0	100
Energy Efficiency	6	0	0	1,617,200	109,657	1,507,543	7
Government Support	1,063	968	91	100,834,251	86,022,780	14,811,471	85
HCFC Individual	312	278	89	12,780,387	11,705,070	1,075,316	92
HCFC phase-out management plan stage 1	357	345	97	27,708,270	26,507,764	1,200,506	96
HCFC phase-out management plan stage 2	225	80	36	44,754,010	22,344,233	22,409,777	50
HCFC phase-out management plan stage 3	16	2	12	4,861,825	837,463	4,024,362	17
HFC Individual	316	220	70	26,753,474	19,552,176	7,201,298	73
Kigali Implementation Plan Stage 1	66	2	3	4,649,415	731,208	3,918,207	16
Other ODS Individual	90	90	100	6,781,350	6,781,350	0	100
Other ODS Sector Plans	32	32	100	3,527,163	3,527,163	0	100
Total	**3,233**	**2,765**	**86**	**481,887,196**	**412,395,942**	**69,491,253**	**86**

* Excluding cancelled and transferred projects

During 2025, the Executive Committee approved 102 new projects for UNEP to implement, including 13 KIP stage I, first tranches, 6 HPMP stage II/III, first tranches, 19 HPMP tranches, ten (10) Additional activities to maintain energy efficiency in the refrigeration servicing sector (decision 89/6) projects, eight (8) new phases of Institutional Strengthening projects and one (1) Emergency assistance for institutional strengthening, 19 Preparation of national inventory of banks of waste-controlled substances (decision 91/66) and the 2026 CAP budget. The following table summarizes the quantitative summary of projects approved for UNEP implementation in 2025.

Sub sector	Project title	Approved projects*	Fund allocated ($ US)*	Project support cost ($ US)*
Agency programme	Compliance Assistance Programme: 2026 budget	1	$ 11,276,970	$ 902,157
HCFC phase out plan	HCFC phase-out management plan (stage I, tranches)	4	$ 362,241	$ 47,091
	HCFC phase-out management plan (stage II, first tranche)	3	$ 649,250	$ 83,153
	HCFC phase-out management plan (stage II, tranches)	14	$ 2,722,962	$323,866
	HCFC phase-out management plan (stage III, first tranche)	3	$ 1,057,932	$ 131,893
	HCFC phase-out management plan (stage III, tranches)	1	$ 116,000	$ 14,612


	HCFC phase-out management plan (stage II): Additional activities to maintain energy efficiency in the refrigeration servicing sector (decision 89/6)	10	$ 1,100,000	$ 140,240
HCFC individual	Verification report on the implementation of stage II of the HCFC phase-out management plan	8	$ 240,000	$ 31,200
	Preparation of an HCFC phase-out management plan (new stage)	5	$ 225,000	$ 29,250
Ozone unit support	Institutional Strengthening projects	9	$ 1,692,377	$ -
Preparation of project proposal	Preparation of national inventory of banks of waste controlled substances and development of a national plan for management of these substances (decision 91/66)	19	$ 1,527,000	$ 198,510
HFC Individual	Verification on the implementation of stage I of the Kigali HFC implementation plan	2	$ 60,000	$ 7,800
	Pilot project to maintain and/or enhance the energy efficiency of replacement technologies and equipment in the context of HFC phase-down (non-investment activities) (decision 91/65)	3	$ 503,000	$ 65,390
	Preparation of a Kigali HFC implementation plan (stage I)	2	$ 180,000	$ 23,400
Kigali Implementation Plan Stage 1	Kigali HFC implementation plan (stage I, first tranche)	13	$ 1,069,114	$ 138,985
	Kigali HFC implementation plan (stage I, first tranche) (PMU)	1	$ 37,400	$ 4,862
	Kigali HFC implementation plan (stage I, second tranche)	1	$ 35,000	$ 4,550
Technical assistance/ support	Enabling activities for HFC phase-down	2	$ 400,000	$ 28,000
	Twinning of national ozone officers and national energy-efficiency policymakers to support Kigali Amendment (phase II)	1	$ 793,200	$ 97,252
Total		**102**	**$ 24,047,446**	**$ 2,272,211**

* Excluding cancelled and transferred projects

II. Project progress in the reporting year

II.1 Activities related to HCFC phase-out

During 2025, UNEP served as an implementing agency for 94 Article 5 countries under HCFC Phase-out Management Plans (HPMPs), supporting the implementation of a total of 153 approved tranches. Of these, UNEP acted as the Lead Agency in 69 countries and as the Cooperating Agency in 25 countries. This extensive engagement underscores UNEP's central role in supporting HCFC phase-out efforts, particularly through the delivery of technical assistance, policy support, capacity-building activities, and compliance-related interventions. The regional distribution of the 94 Article 5 countries receiving UNEP support is presented in the figure below:

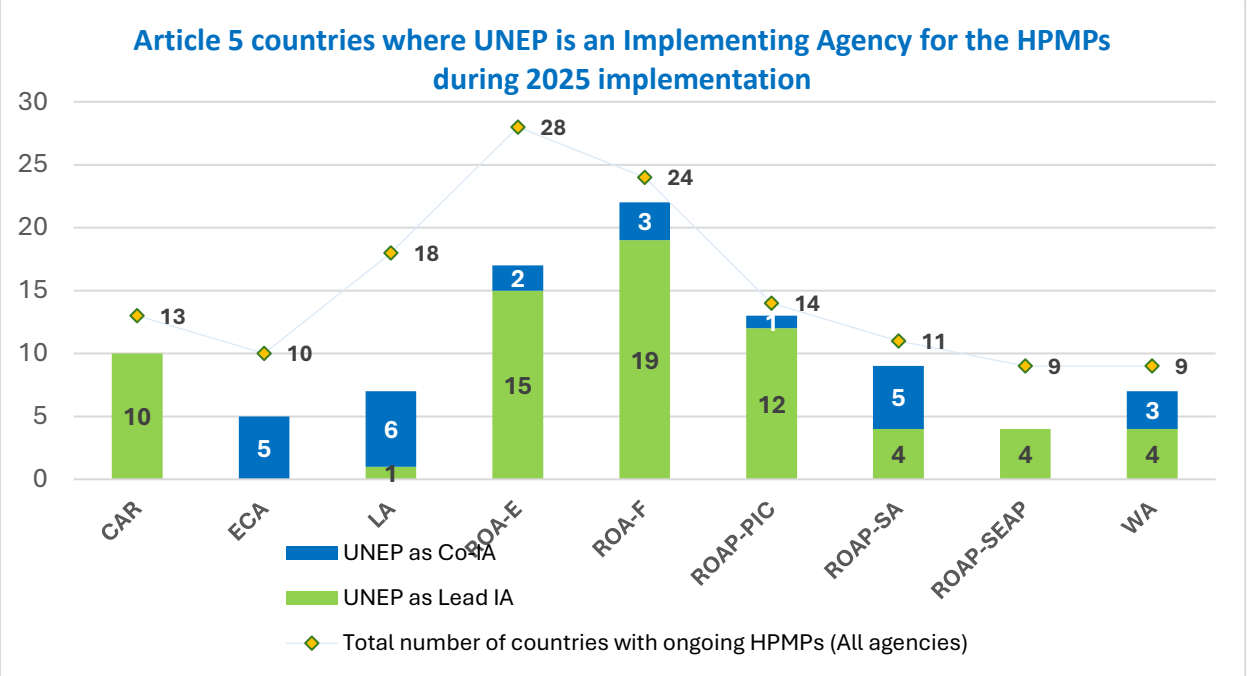

HCFC phase-out projects by type and implementation status:


HCFC phase-out projects	Approved in 2025	Under implementation as of the end of 2025	Completed in 2025	Financially completed in 2025
HPMP tranches (exc. Additional activities for EE under decision 89/6)	*25*	*129*	*4*	*20*
Verification report on the implementation of the HPMP	*8*	*22*	*-*	*11*
Preparation of an HPMP stage II/III	*5*	*10*	*-*	*6*

Countries continued to phase-out HCFCs, achieving the 67.5% reduction target in 2025. Through the HPMP projects, countries strengthened regulatory systems, conducted extensive national capacity-building activities for enforcement and RAC servicing technicians, updated training materials, improved stakeholder coordination, enhanced awareness efforts, and progressed towards the full HCFC phase-out. In the reporting period, 7 (seven) countries had a new stage of their HPMP approved, UNEP is a lead agency of the three (3) countries and cooperating agency for the remaining four (4).

II.2 Activities related to HFC phase-down

As of December 2025, a total 64 KIP Preparation projects were approved for UNEP, including one regional project for 12 Pacific Island Countries, and 42 of them have been completed. In 2025, UNEP submitted 13 KIP stage I project proposals to the 96th and 97th ExComs. In addition, one KIP stage I proposal for Group-2 country was submitted, which was deferred to future meetings. With this, during 2025 implementation period, UNEP was an implementing agency of 58 Article 5 countries for their KIP stage I projects, out of which UNEP was the Lead Agency for 39 countries and the Cooperating Agency for 19 countries. Where UNEP is

as the Lead Agency, 36 of the countries are LVCs or funded as LVC under KIP and 3 are non-LVCs. The following graph shows the regional distribution of these projects:

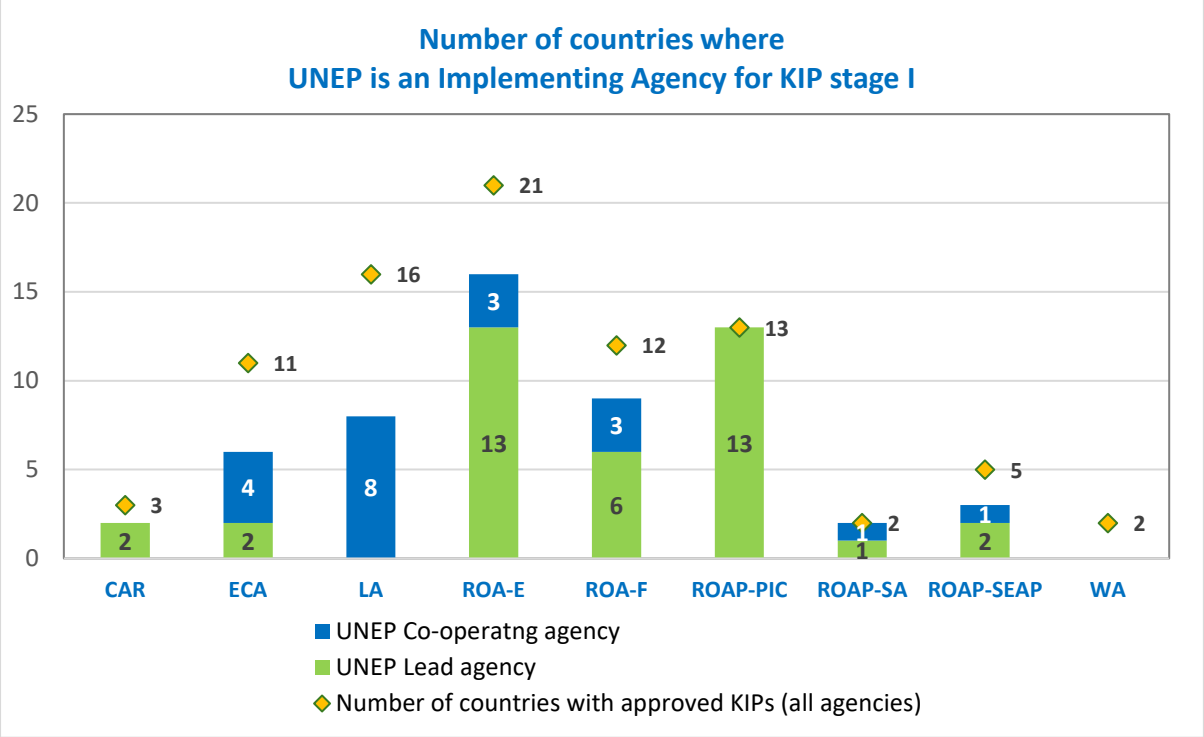

HFC phase-down projects by type and implementation status:

HFC phase-down projects	Approved in 2025	Under implementation as of the end of 2025	Completed in 2025	Financially completed in 2025
KIP stage I, tranches	*13*	*57*	-	*2*
Verification report on the implementation of stage I of the KIP	*2*	*2*	-	-
Preparation of a KIP stage I	*2*	*22*	*1*	*16*
Enabling Activities for HFC phase-down	*2*	*3*	-	-

Preparation of Kigali Implementation Plans (KIP) Stage I: Countries strengthened their preparedness for the HFC phase-down through enhanced awareness and understanding of HFC licensing and quota systems, supported by stakeholder consultations and national workshops. UNEP worked closely with national counterparts to validate and refine survey findings, assess policy and regulatory gaps, identify training and capacity-building requirements, and evaluate the market penetration and availability of low-global-warming-potential alternatives. Despite delays in some countries resulting from data availability challenges and slower-than-anticipated recruitment processes, most projects advanced satisfactorily during the reporting period. Several KIP Stage I project proposals were finalized and submitted, or prepared for submission, to upcoming meetings of the Executive Committee.

KIP Stage I implementation: Countries continued to advance the implementation of Stage I of their KIPs by operationalizing and strengthening HFC licensing and quota systems in support of national HFC phase-down obligations. Key activities included the delivery of

training programmes on good servicing practices for refrigeration and air-conditioning (RAC) technicians, with a particular emphasis on the safe handling, installation and servicing of zero- and low-global-warming-potential alternatives, including flammable refrigerants. Countries also updated technical and training materials, developed and strengthened safety standards and guidelines, enhanced inter-institutional and stakeholder coordination mechanisms, and expanded public awareness and outreach activities. Gender considerations were systematically integrated across implementation activities to promote inclusive participation and capacity development.

Despite overall satisfactory progress, implementation was affected by several common challenges, including lengthy administrative procedures related to the approval and signing of Small-Scale Funding Agreements (SSFAs), regulatory gaps requiring the adoption or revision of decrees, standards and supporting legislation, inconsistencies in HFC data collection and reporting systems, and limited technical capacity in specialized RAC subsectors. Countries continued to address these challenges through targeted policy support, capacity-building interventions and strengthened stakeholder engagement, laying the foundation for sustained compliance with Kigali Amendment commitments.

II.3 Activities related to energy efficiency

Energy efficiency projects by type and implementation status:

Energy efficiency projects	Approved in 2025	Under implementation as of the end of 2025	Completed in 2025	Financially completed in 2025
Additional activities to be included under the HPMPs for low-volume-consuming countries to maintain energy efficiency for the servicing sector (decision 89/6(b))	*10*	*47*	*3*	*2*
Pilot projects for energy efficiency (decision 91/65)	*3*	*5*	-	-

As of December 2025, UNEP was implementing 48 projects approved under the Additional activities to maintain energy efficiency in the refrigeration servicing sector for LVCs (decision 89/6(b)), including one regional project for the Pacific Island Countries and one project that has since been completed. Overall, 66 of the 96 eligible countries have secured funding approvals for these activities.

Implementation progressed steadily during the reporting period, with countries strengthening inter-institutional coordination and advancing a broad range of technical and policy measures to support improved energy efficiency in RAC sector. Key achievements included the development of awareness-raising materials, consumer behavior assessments, extensive stakeholder consultations, the engagement of national and international experts, and the integration of energy-efficiency considerations into RAC servicing training programmes. Countries also delivered a range of capacity-building activities, including training workshops on minimum energy performance standards (MEPS), energy-labelling schemes, and the introduction and promotion of energy-efficient, low-global-warming-potential (GWP) technologies.

Most projects focused on the development, strengthening or implementation of MEPS and energy-labelling frameworks for residential refrigeration and air-conditioning equipment. Progress in these areas typically requires comprehensive technical assessments, market and regulatory analyses, stakeholder consultations, standards development, and the adoption or revision of supporting policy and regulatory frameworks. Consequently, implementation timelines have often been influenced by the complexity of these processes.


Challenges remain, particularly in LVC countries that rely exclusively on imported RAC equipment. In many cases, limited institutional capacity and shortages of specialized technical expertise in energy-efficiency policy and standards development have constrained implementation. As a result, countries have frequently depended on international technical assistance to undertake specialized analyses and support the development of MEPS and energy-labelling frameworks. Notwithstanding these challenges, the projects have continued to strengthen national capacities and establish the policy and institutional foundations necessary to enhance energy efficiency in the RAC sector while supporting climate and ozone protection objectives.

II.4 Activities related to national inventories of banks of waste-controlled substances

As of December 2025, a total of 71 Preparation of national inventory of banks of waste-controlled substances (decision 91/66) projects were approved for UNEP for implementation, as lead implementing agency for 67 and cooperating agency for four (4) projects. UNEP is an implementing agency for 70 countries, which represents 55% of the total number of countries that have this project approved. 19 of these projects were approved in 2025.

Projects related to national inventories of banks of waste-controlled substances	Approved in 2025	Cumulative approved as of December 2025	Under implementation as of the end of 2025	Completed in 2025
Preparation of national inventories of banks of waste-controlled substances (decision 91/66)	*19*	*71**	*69***	*1*

**including one Regional project for Pacific Island Countries*
***one project was closed*

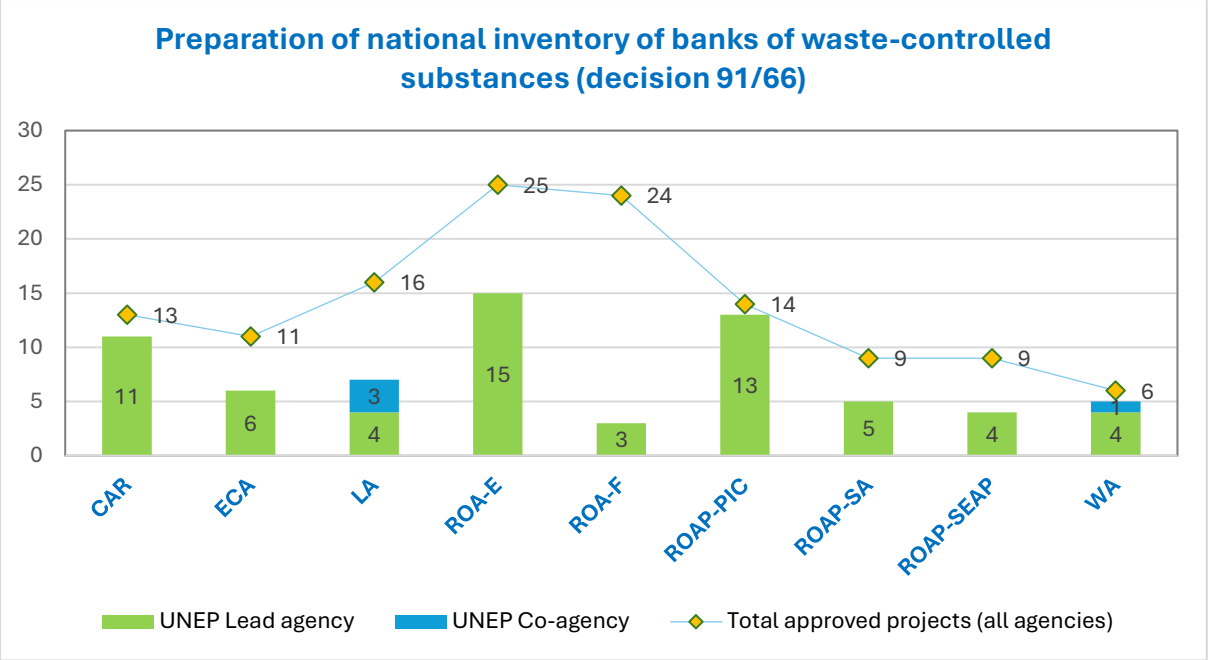

Preparation of national inventories of banks of waste-controlled substances (decision 91/66) presented a number of implementation challenges, reflecting the complex and emerging nature of this area of work. These activities require countries to identify, quantify and assess banks of waste-controlled substances across a range of sectors and stakeholders, while strengthening understanding of refrigerant lifecycle management and the associated policy, regulatory and institutional frameworks needed to support their environmentally sound management.

During implementation, countries encountered a range of technical, institutional and capacity-related challenges. A key constraint was the limited availability of specialized expertise in areas such as refrigerant lifecycle management, inventory development, waste management and destruction technologies. In several cases, recruitment processes had to be repeated due to difficulties in identifying suitably qualified local and/or regional consultants, which affected implementation timelines. The preparation activities also highlighted existing gaps in national regulatory and institutional frameworks related to chemicals management, waste management and refrigerant lifecycle management, as well as challenges associated with the availability, accessibility and quality of relevant data.

Progress reports submitted by countries consistently underscored the need for further technical capacity development, strengthening of policy and regulatory frameworks, and enhanced access to specialized expertise to support the effective and timely completion of these activities. In response, UNEP, through its Compliance Assistance Programme (CAP), organized a series of thematic meetings and knowledge-sharing events during the network meetings on refrigerant lifecycle management. These meetings provided countries with opportunities to exchange experiences and learn from international experts and practitioners on issues such as the transboundary movement of waste-controlled substances, extended producer responsibility (EPR) approaches, mandatory refrigerant recovery schemes, and technologies and business models for the collection, reclamation and destruction of high-global-warming-potential substances.

In light of the implementation challenges identified and the additional time required to complete technical assessments and stakeholder consultations, UNEP requested implementation extensions for 16 projects at the 97th Meeting of the Executive Committee held in December 2025. During the reporting period, UNEP completed one project and is supporting the finalization and submission of the corresponding national inventory and national action plan.

II.5 Activities related to Institutional Strengthening projects


Institutional Strengthening projects continued to serve as the cornerstone of national implementation of the Montreal Protocol, providing the institutional capacity and coordination mechanisms required for countries to meet their compliance obligations and sustain the achievements of phase-out and phase-down programmes. As of December 2025, UNEP was the implementing agency for Institutional Strengthening projects in 99 Article 5 countries, comprising 80 low-volume-consuming (LVC) countries and 19 non-LVC countries.

Through these projects, UNEP supported National Ozone Units in strengthening national ownership and leadership of Montreal Protocol activities, ensuring effective coordination among government agencies and stakeholders, and integrating ozone-related objectives into broader national policies and development priorities. Particular emphasis was placed on empowering countries to lead the planning, implementation and monitoring of activities in accordance with their national circumstances and priorities.

During the reporting period, UNEP assisted NOUs in maintaining and strengthening licensing and quota systems for controlled substances and HFCs. UNEP also supported countries in meeting their Country Programme and Article 7 reporting obligations through strengthened data collection, verification and reporting processes, recognizing the critical role of reliable data in informed decision-making, policy development and compliance monitoring.

In addition, IS projects enabled countries, particularly LVCs, to coordinate and oversee the implementation of HPMPs, KIPs, Energy-efficiency activities and other Montreal Protocol initiatives.

The following graph shows the regional distribution of the UNEP assisted IS projects:

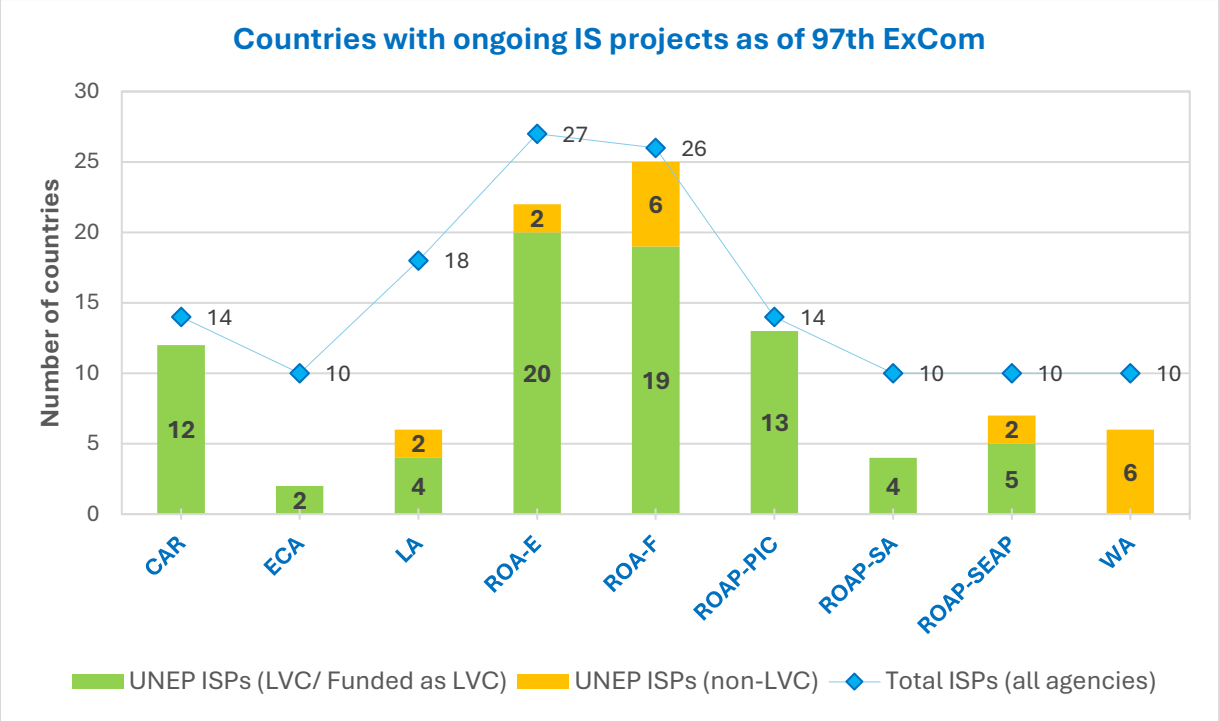

In 2025, UNEP had nine (9) new IS projects, including one (1) Emergency assistance for institutional strengthening for Maldives, approved for implementation:

Region	Total number of countries assisted by UNEP for IS in 2025	Number of IS renewals approved in 2025
CAR	12	1
ECA	2	-
LA	6	1
ROA-E	23	3
ROA-F	25	3
ROAP-PIC	13	-
ROAP-SA	4	1
ROAP-SEAP	8	-
WA	6	-
Total	**99**	**9**

III. Project completion in the reporting year

In 2025, UNEP completed 70 projects, consisting of 16 HPMP tranches, three (3) Additional activities for energy efficiency (decision 89/6), 10 verification reports, five (5) preparations of new stages of HPMP, 14 KIP Preparations, one (1) KIP stage I tranche, 20 phases of IS project, and the phase I of the Twinning of national ozone officers and national energy efficiency policy makers to support Kigali Amendment objectives project. 29 of these projects were financially completed.

Cluster	Sector	Number of projects completed	Phase-out	
			ODP/MT	CO2-eq tonnes

Government Support	National Ozone Unit	20		
HCFC Individual	SERVCEE-89/6	1		
HCFC Individual	Servicing	5		
HCFC Individual	Verification	10		
HCFC phase-out management plan stage 1	Servicing	2		
HCFC phase-out management plan stage 2	SERVCEE-89/6	2		
HCFC phase-out management plan stage 2	Servicing	14		
HFC Individual	Disposal	1		
HFC Individual	Servicing	14		
Kigali Implementation Plan Stage 1	Servicing	1		
Total		**70**		

IV. Gender activities

UNEP continues to promote empowerment of women through CAP activities in line with UNEP's Policy and Strategy for Gender Equality and the Environment and the Multilateral Fund's Operational Policy on Gender Activities for Multilateral Fund-supported Projects. OzonAction's Gender Core Team provides internal guidance to the CAP regional teams, monitors, and reports on gender activities in the Multilateral Fund supported projects. OzonAction operationalized its own internal plan which provides a comprehensive approach to women empowerment in its work, including both institutional (internal) and programmatic (external) actions. As part of the latter, UNEP has included gender considerations in all projects approved since June 2020 as per Multilateral Fund requirements.

UNEP analyzed 33 UNEP-lead project requests for Stage 1 of Kigali Implementation Plans (KIPs), submitted to the Executive Committee meetings between 2023 and 2026. The findings show strong integration of gender considerations across UNEP-led KIP Stage I submissions, while highlighting opportunities to strengthen compliance with gender assessment requirements.

- All 33 UNEP-led KIP Stage I submissions included gender-responsive activities and indicators and addressed the Multilateral Fund's Operational Policy on Gender. This indicates that gender considerations have been systematically incorporated into projects approved during the period under review.
- Of the 30 countries that submitted Stage I KIP requests from the 94th meeting onward, all incorporated gender-responsive results frameworks and indicators. However, compliance with the requirement to conduct and submit a gender assessment report remained limited. Two submissions included the required gender assessment and report, while seven submissions planned or committed to developing a Gender Action Plan (GAP). Additionally, 20 of the 33 submissions included dedicated budget allocations for gender activities.
- Several countries demonstrated efforts to engage gender-related stakeholders during project planning and implementation. Twelve submissions specifically proposed involving gender experts, women's associations, NGOs, or government bodies working on gender in project activities and decision-making processes. In addition, six submissions encouraged greater participation of women in stakeholder consultations and leadership discussions

related to project implementation.

- The analysis indicates substantial efforts to strengthen capacity for gender-responsive project implementation. Common measures included
    a) Increasing women's participation in RAC technical training programmes (24 submissions).
    b) Promoting participation of women in customs and enforcement training (16 submissions).
    c) Supporting female technicians through specialized training, certification, business development support, and leadership opportunities.
    d) Collecting sex-disaggregated data (26 submissions) to improve monitoring, reporting, and evidence-based decision-making.

These activities contribute to building institutional and national capacity to integrate gender considerations throughout the project cycle.

V. Risk assessment

UNEP have introduced a new systematic risk monitoring framework for its implementing partners as part of its enhanced risk assessment and partner oversight processes. This initiative was developed in response to recommendations from the UN Board of Auditors, which, in its report A/80/5/Add.7 (paragraph 70), recommended that UNEP establish a systematic monitoring mechanism within its implementation agreement management systems to identify and flag risks associated with partner engagements.

Under the framework, risks are identified through a series of automated and structured checks, commonly referred to as Red Flags. These are triggered by factors such as overdue financial and audit reports, non-compliance with legal instrument clauses, adverse budget variances, unresolved ineligible expenditures, and adverse audit findings. By embedding these checks early in the partnership lifecycle, UNEP is able to proactively identify emerging risks, assess the suitability of partners for specialized technical work, and implement appropriate mitigation measures where necessary.

As a result, the systematic risk monitoring framework strengthens UNEP's overall risk assessment and monitoring capabilities, reduces operational and fiduciary vulnerabilities, and supports the more effective, accountable, and secure delivery of environmental programmes.

Some countries often face delays in implementation due to administrative bottlenecks, lengthy government clearance procedures, and changes in institutional leadership that interrupt decision-making. Political transitions, regional instability, and security concerns can further disrupt planning, restrict field activities, or limit access to certain areas. In many cases, these external and administrative factors create uncertainty, slow coordination, and ultimately push project timelines beyond the original schedule.

UNEP proactively manages implementation delays through regular engagement and targeted follow-ups with NOUs, continuous situational analysis, and the timely adjustment of workplans, implementation approaches, and timelines as necessary. To address administrative bottlenecks and sustain momentum, UNEP provides tailored technical and strategic support,

including management-level missions to strengthen inter-agency coordination, facilitate high-level government engagement, and reinforce institutional commitment. UNEP also convenes stakeholder consultations and coordination meetings to identify and resolve implementation challenges, build consensus among relevant actors, and accelerate decision-making. Where appropriate, UNEP works with national counterparts to develop mitigation measures, strengthen project management capacity, and establish clear implementation roadmaps that help maintain progress despite political, administrative, or security-related disruptions.

VI. Performance indicators

Type of indicator	Short title	Calculation	Targets	Achievements	Calculation
Planning-Approval	Tranches approved	Number of tranches approved vs. those planned*	80	40	Number of tranches approved vs. those planned*
Planning-Approval	Individual projects/ activities approved	Number of projects/activities approved vs. those planned (including project preparation activities)	96	62	Number of projects/activities approved vs. those planned (including project preparation activities)
Implementation	Funds disbursed	Based on estimated disbursement in progress reports	23,701,624	23,194,156	Based on estimated disbursement in progress reports
Implementation	ODS phase-out for HCFC-related projects	ODS phase-out for HCFC-related projects in ODP tonnes vs. those planned per progress reports	107.9 ODP tonnes	-	ODS phase-out for HCFC-related projects in ODP tonnes vs. those planned per progress reports
Implementation	HFC phase-down for HFC-related projects	HFC phase-down for HFC-related projects in CO2-eq tonnes vs. those planned per progress reports	zero CO2-eq tonnes	-	HFC phase-down for HFC-related projects in CO2-eq tonnes vs. those planned per progress reports
Implementation	Project operational completion	Project operational completion vs. planned in progress reports for all activities (excluding project preparation)**	58	51	Project operational completion vs. planned in progress reports for all activities (excluding project preparation)**
Implementation	Gender mainstreaming	Operational policy on gender mainstreaming applied to all approved projects	100%	100%	Operational policy on gender mainstreaming applied to all approved projects
Administrative	Speed of financial completion	The extent to which projects are financially completed within 12 months after project operational completion	12 months after operational completion	12 months	The extent to which projects are financially completed within 12 months after project operational completion
Administrative	Timely submission of project completion reports	Timely submission of project completion reports based on the progress report	3	2	Timely submission of project completion reports based on the progress report

Administrative	Timely submission of progress reports and business plans	Timely submission of progress reports and business plans and responses unless otherwise agreed	On time	On time	Timely submission of progress reports and business plans and responses unless otherwise agreed

*Armenia tranche was approved but later transferred to UNIDO

-Several countries experienced public health vulnerabilities/outbreaks or prolonged political and/or security instability in the surrounding region that affected the timely submission of planned projects. These include Bahrain, Burundi, Democratic Republic of Congo, Iraq, Mali, South Sudan, Syrian Arab Republic, Tunisia, and Uganda.

VII. Country highlights

Belize, Caribbean - Belize has demonstrated significant performance in 2025 in the implementation of projects and policies. Firstly, the NOU has conducted nationwide capacity building, training 450 RAC technicians on alternative technologies. Secondly, the country finalized and established two (2) statutory instruments: SI No. 95 (Environmental Protection (Ozone Layer Protection) Regulations) and SI No. 96 (Refrigeration Technicians (Licensing) Regulations), which strengthen enforcement of HCFCs and legally establish enforcement of HFCs and set licensing requirements for RAC technicians, respectively. Together, the SIs provide the national legal basis for HFC phase-down and provide the national standards and licensing measures enforceability under the national law. Further, three (3) mandatory standards were developed collaboratively with the Belize Bureau of Standards: BZS 34:2025 and BZS 35:2025, which set Minimum Energy Performance Standards (MEPS) and mandatory energy labelling for refrigerators, freezers, and air conditioners. Standard BZS 28:2025 provides specifications for the safe storage, handling, and transport of carbon dioxide, supporting the initial entry of an ultra-low-GWP refrigerant into the national market. Finally, during this period, the Country completed one (1) Project (ISP Phase XI) and maintained strong implementation progress on five (5) projects through progress on agreed project activities and the submission of reports to UNEP in a timely manner.

Bolivia, Latin America - In 2025, Bolivia made significant progress in implementing the Kigali Amendment and promoting sustainable refrigeration technologies. The Government adopted Administrative Resolution VMABCCGDF No. 122/2025, establishing the national HFC import quota allocation framework, and initiated the integration of the electronic licensing system for controlled substances into the Single Window for Foreign Trade (VUCE). The country also enabled the legal importation of R-290, with the first customs clearance completed in December 2025. Furthermore, Ministerial Resolution No. 821/2025 approved an occupational standard for refrigeration technicians working with hydrocarbons, incorporating competencies for the safe handling of flammable refrigerants, risk management and good servicing practices.

Cambodia, Southeast Asia - During the reporting period, the NOU achieved significant progress in HFC and HCFC management, regulatory strengthening, and capacity building. Key achievements included the enhancement of the HFC licensing and quota system through integration with the National Single Window System and the adoption of CO_2-equivalent tracking to improve quota monitoring and enforcement; the enactment of a Ministerial Declaration on HFC quota allocation procedures in November 2025 to ensure greater transparency, consistency, and accommodation of new importers while prioritizing grandfather

importers; the integration of energy efficiency modules into RAC servicing technician training; and the institutionalization of competency-based assessment for RAC technicians in collaboration with TVET and Ministry of Labour. The NOU also successfully completed the HPMP Stage I, fifth tranche, conducted HCFC verification, and secured approval of the sixth tranche in 2025.

China, South Asia – China delivered two GSP trainings in Guangzhou in 2025 as part of the South-South cooperation. The first, held on 7–9 January, gathered 18 participants from South Asia, Southeast Asia, and West Asia. The second, held on 3–7 November, hosted 20 participants from 14 countries across Asia-Pacific and Africa. In April, China organized the 14th national Ozone2Climate Technology Roadshow and Industry Roundtable at China Refrigeration Expo 2025 in Shanghai and Beijing, featuring a 500 m² booth, over 40 enterprises showcasing R32, R290, CO_2, NH_3 and other low-GWP technologies, and attracting more than 10,000 visitors. In the same month, the State Council of China approved the National Implementation Plan for the Montreal Protocol on Substances that Deplete the Ozone Layer (2025–2030). This strategic plan outlines the roadmap for the complete phase-out of HCFCs by 2030 and sets a target for a 10% reduction in Hydrofluorocarbons (HFCs) by 2029.China maintained strong import/export controls and active iPIC use to effectively prevent potential illegal trade of ODS, issuing 2,364 ODS export permits and rejecting 23 batches were rejected through iPIC mechanism, preventing potential illegal trade of 480 metric tonnes of ODS. On September 16, 2025, China held a commemorative event marking the 40th anniversary of the adoption of the Vienna Convention for the Protection of the Ozone Layer and the 2025 Worl Ozone Day, attended by approximately 200 guests including Executive Secretary of the Ozone Secretariat, Chief Officer of the Multilateral Fund Secretariat, representatives from the Multilateral Fund implementing agencies, officials from relevant departments of the Ministry of Foreign Affairs and the General Administration of Customs. The following day, FECO/MEE convened an HPMP Coordination Meeting with about 30 representatives from implementing agencies, bilateral partners, research institutions, and industry associations.

Georgia, Europe and Central Asia - The year 2025 was marked by significant progress in updating national legislation, including import-permit allocation rules and environmental requirements for the servicing, maintenance and labeling of RACHP equipment and refrigerant containers. Georgia also introduced a ban on the import of second-hand equipment operating on ODSs. Three new projects, namely, KIP stage I, first tranche, Preparation of national inventory of banks of waste-controlled substances and development of a national plan for management of these substances (decision 91/66), and Pilot project to maintain and/or enhance the energy efficiency of replacement technologies and equipment in the context of HFC phase-down (non-investment activities) (decision 91/65), were approved in 2025. To foster regional cooperation and strengthen partnership to support the Montreal Protocol, Georgia hosted the Joint Europe and Central Asia- West Asia meeting of Montreal Protocol Officers and Environmental Inspectors, Batumi, Georgia, 17-19 June 2025 and the CCAC workshop on life-cycle refrigerant management, Batumi, Georgia, 20 June 2025.

Pacific Island Countries, consisting of Cook Islands, Fiji, Kiribati, Marshall Islands (Republic of), Micronesia (Federated States of), Naoero, Niue, Palau, Samoa, Solomon Islands, Tonga,

Tuvalu, and Vanuatu, achieved several standout results that go well beyond routine implementation. UNEP supported the region in reviewing commonly used HFCs to assign individual HS codes for HFCs and mixtures and worked with the Oceania Customs Organization to agree on integration of individual HS codes into the PACHS28. UNEP assisted all 14 PICs to develop HFC quota and import-tracking mechanism, which has improved accuracy and timeliness of Country Programme and Article 7 data reporting. Fiji enacted a full ban on HCFC-based equipment, and Palau became the first PIC to legislate a ban on R-410A based residential air-conditioners and HFC-134a based domestic refrigerators, effective 1 January 2027 — a major regulatory milestone. The region further distinguished itself through strong north–south and south–south cooperation, with Australia providing advanced technical sessions and Fiji institutionalizing mandatory iPIC consultations.

VIII. Administrative matters and other issues

VIII.1 Meetings attended

UNEP used a combination of face-to-face meetings with online services such as video conferencing, telephones, and emails/chats to deliver global activities. UNEP, as a part of its CAP services, organized Regional Network meetings in all regions for all NOUs to address priority issues, e.g. data reporting, Kigali Amendment, HFCs consumption in the context of KIP preparation, the development of national inventories of banks of used or unwanted controlled substances, customs codes, monitoring, reporting, verification and enforcement (MRVE), standards, licensing and quota systems, illegal trade, good servicing practices, safety for flammable refrigerants, policy developments, energy efficiency, etc.

In 2025, UNEP organized a large number of regional network and thematic meetings as well as partnership activities through CAP. The details of the meetings are reported in the CAP progress report.

VIII.2 Implementing agency and other co-operation

UNEP's work under the Multilateral Fund is performed in close cooperation and coordination with the Multilateral Fund Secretariat, Ozone Secretariat, the other Implementing Agencies (UNDP, UNIDO, World Bank), bilateral agencies, and other partners at the international, regional, and national levels. Examples include:

- Regional Network, thematic and other meetings. During the period 1 January – 31 December 2025, UNEP organized a large number network/thematic meetings for NOUs and other national stakeholders. Documentation from many of the events listed below are available on the OzonAction Meeting Portal at www.ozonactionmeetings.org.
- HPMP implementation. UNEP implements many of its projects on the ground in countries jointly with other Implementing Agencies, where each agency co-implements complementary parts of a single project. In 2025 UNEP was the Lead Agency for the HPMP implementation for 69 Article 5 countries, and the Cooperating Agency for the HPMPs of 25 countries. UNEP cooperated with UNIDO in 51 countries, UNDP in 24

countries, Australia in 12 countries, Germany in 2 countries, and Japan in 2 countries for HPMP implementation.

- UNEP implements 58 KIP stage I projects including one regional KIP for 12 PICs. UNEP implements these projects with other agencies, 39 UNEP as the Lead Agency and 19 UNEP as the Cooperating Agency. UNEP implemented 28 of KIP stage I projects with UNIDO, 16 with UNDP, 1 with World Bank, 12 with Australia, and 1 with Germany.

VIII.3 Other issues

N/A.

Annex I: Summary Tables

1. *A summary of a few sentences should precede each table. This enables the agencies to present a summary of all projects that have been completed or are ongoing since the Fund's inception.*

(a) Annual summary data

Year approval	Number of Approvals	Number of completed	Per cent completed (%)	Approved funding plus adjustments (US$)	Funds disbursed (US$)	Balance (US$)	Per cent of funds disbursed (%)
1991	11	11	100%	1,372,335	1,372,335	0	100
1992	15	15	100%	1,711,000	1,711,000	0	100
1993	49	49	100%	4,194,343	4,194,343	0	100
1994	58	58	100%	4,231,169	4,231,169	0	100
1995	50	50	100%	4,047,683	4,047,683	0	100
1996	47	47	100%	3,345,039	3,345,039	0	100
1997	87	87	100%	7,962,291	7,962,291	0	100
1998	64	64	100%	4,669,124	4,669,124	0	100
1999	87	87	100%	6,368,983	6,368,983	0	100
2000	85	85	100%	6,300,398	6,300,398	0	100
2001	59	59	100%	7,411,159	7,411,159	0	100
2002	72	72	100%	9,469,401	9,469,401	0	100
2003	78	78	100%	11,165,394	11,165,394	0	100
2004	99	99	100%	12,362,652	12,362,652	0	100
2005	72	72	100%	12,339,483	12,339,483	0	100
2006	108	108	100%	12,731,484	12,731,484	0	100
2007	79	79	100%	14,611,111	14,611,111	0	100
2008	132	132	100%	17,875,070	17,875,070	0	100
2009	115	115	100%	17,250,876	17,250,876	0	100

2010	79	79	100%	14,356,674	14,356,674	0	100
2011	100	100	100%	16,782,433	16,782,434	-1	100
2012	80	80	100%	16,086,261	16,086,261	0	100
2013	90	90	100%	14,152,112	14,152,112	-1	100
2014	74	74	100%	12,328,954	12,328,953	1	100
2015	180	180	100%	21,169,099	21,169,098	1	100
2016	95	95	100%	19,552,807	19,552,805	2	100
2017	88	88	100%	15,532,086	15,532,085	1	100
2018	173	172	99%	23,738,631	23,651,458	87,173	100
2019	110	107	97%	14,871,180	14,784,683	86,496	99
2020	130	107	82%	15,165,976	13,179,022	1,986,954	87
2021	126	109	87%	21,847,003	20,770,089	1,076,914	95
2022	101	75	74%	22,864,789	19,382,170	3,482,618	85
2023	125	36	29%	27,139,094	17,048,683	10,090,412	63
2024	213	6	3%	42,833,659	13,954,105	28,879,554	33
2025	102	0	0%	24,047,446	246,316	23,801,130	1
Total	**3233**	**2765**	**86%**	**481,887,196**	**412,395,942**	**69,491,253**	**86**

(b) Cumulative completed investment projects

A summary of a few sentences should precede each table. This enables the agencies to present a summary of all projects that have been completed or are ongoing since the Fund's inception.

Item	Number of completed	Approved funding plus adjustments (US$)	Per cent of funds disbursed (%)	Consumption Phased Out (ODP tonnes)	Production Phased Out (ODP tonnes)	Consumption Phased Out (metric tonnes)	Production Phased Out (metric tonnes)	Consumption Phased Out (Co2-eq tonnes)	Production Phased Out (CO2-eq tonnes)	Average number of months from approval to first disbursement	Average number of months from approval to	Cost effectiveness to fund (US$/kg.)

											completion	
Total	**0**	**0**	**0**	**0.0**	**0.0**	**0.0**	**0.0**	**0**	**0**	**0**	**0**	**0.00**
Region												
Sector												

(c) Cumulative completed non-investment projects

A summary of a few sentences should precede each table. This enables the agencies to present a summary of all projects that have been completed or are ongoing since the Fund's inception.

Item	Number of projects	Approved funding plus adjustments (US$)	Per cent of funds disbursed (%)	Average number of months from approval to first disbursement	Average number of months from approval to completion
Total	**2,373**	**370,519,827**	**100**	**12**	**37**
Region					
Africa	929	69,043,270	100	12	35
Asia and the Pacific	674	69,164,699	100	13	39
Europe	101	7,391,731	100	9	32
Global	204	194,273,950	100	5	23
Latin America and the Caribbean	465	30,646,176	100	17	46
Sector					
Aerosol	11	882,689	100	7	37
Air-Conditioning	3	536,684	100	11	39
Compliance Assistance Programme	23	175,060,139	100	1	16
Disposal	2	190,040	100	5	70
Enabling activities	93	9,205,409	100	13	44

Firefighting	17	807,640	100	11	33
Foam	1	43,014	100	19	96
Fumigant	46	2,654,864	100	8	28
National Ozone Unit	968	80,417,149	100	13	37
Pre-CAP	164	22,652,562	100	4	20
Project monitoring and coordination	1	48,951	100	7	25
Refrigeration	193	9,094,713	100	16	52
SERVCEE-89/6	3	290,000	85	12	26
Servicing	645	61,263,321	99	14	42
Solvent	2	198,860	100	4	34
Survey	83	4,252,536	100	11	25
Verification	118	2,921,255	99	14	27

(d) Cumulative completed project preparation activities

A summary of a few sentences should precede each table. This enables the agencies to present a summary of all projects that have been completed or are ongoing since the Fund's inception.

Region	Number of projects	Approved funding plus adjustments (US$)	Per cent of funds disbursed (%)	Average number of months from approval to first disbursement	Average number of months from approval to completion
Total	**392**	**17,451,780**	**99**	**11**	**31**
Region					
Africa	177	7,640,039	99	12	31
Asia and the Pacific	106	5,959,925	98	11	32
Europe	21	941,903	98	10	19
Global	2	158,412	100	8	39
Latin America and the Caribbean	86	2,751,501	99	11	29
Sector					
Disposal	1	80,000	97	14	24
Refrigeration	47	1,167,465	100	10	25
Servicing	250	13,257,741	98	13	34

Technical Assistance	94	2,946,574	100	7	25

(e) Cumulative ongoing investment projects

A summary of a few sentences should precede each table. This enables the agencies to present a summary of all projects that have been completed or are ongoing since the Fund's inception.

Item	Number of Projects	Approved funding plus adjustments (US$)	Funds Disbursed (US$)	Per cent of funds disbursed (%)	Number of projects disbursing	Per cent of projects disbursing (%)	Average of months from approval to first disbursement	Average number of months from approval to planned completion	Average length of delay in project planned completion	Overall cost-effectiveness to the Fund (US$/kg)
Total	**0**	**0**	**0**	**0**	**0**	**0%**	**0**	**0**	**0**	**0.00**
Region										
Sector										

(f) Cumulative ongoing non-investment projects

A summary of a few sentences should precede each table. This enables the agencies to present a summary of all projects that have been completed or are ongoing since the Fund's inception.

Region	Number of Projects	Approved funding plus adjustments (US$)	Funds Disbursed (US$)	Per cent of funds disbursed (%)	Number of projects disbursing	Per cent of projects disbursing (%)	Average number of months from approval to first disbursement	Average number of months from approval to planned completion	Average length of delay in project planned completion
Total	**367**	**86,021,589**	**24,617,172**	**29**	**181**	**49%**	**17**	**43**	**6**
Region									
Africa	141	20,505,854	5,640,122	28	61	43%	17	37	3
Asia and the Pacific	141	33,463,890	7,699,521	23	76	54%	17	52	8
Europe	13	1,649,110	416,411	25	8	62%	12	37	1
Global	3	23,261,500	9,594,013	41	1	33%	0	22	4
Latin America and the Caribbean	69	7,141,235	1,267,105	18	35	51%	22	38	7

Sector									
Compliance Assistance Programme	2	22,468,300	9,594,013	43	1	50%	0	18	6
Enabling activities	3	450,000	0	0	0	0%	0	20	0
National Ozone Unit	95	20,417,102	5,743,990	28	61	64%	18	40	4
Project monitoring and coordination	6	135,428	29,950	22	2	33%	10	41	5
SERVCEE-89/6	44	3,918,000	406,277	10	17	39%	14	47	2
Servicing	193	37,912,759	8,795,987	23	95	49%	18	45	7
Verification	24	720,000	46,955	7	5	21%	20	31	12

(g) Cumulative ongoing project preparation activities

A summary of a few sentences should precede each table. This enables the agencies to present a summary of all projects that have been completed or are ongoing since the Fund's inception.

Item	Number of projects	Approved funding plus adjustments (US$)	Funds Disbursed (US$)	Per cent of funds disbursed (%)	Average number of months from approval to first disbursement	Average of months from approval to planned completion	Average length of delay in project planned completion
Total	**101**	**7,894,000**	**1,368,260**	**17**	**13**	**34**	**10**
Region							
Africa	29	2,606,000	557,580	21	10	37	12
Asia and the Pacific	42	3,086,000	467,793	15	16	35	12
Europe	6	475,000	176,131	37	15	32	8
Latin America and the Caribbean	24	1,727,000	166,756	10	12	30	7
Sector							
Disposal	69	5,312,000	644,172	12	11	32	7
Servicing	32	2,582,000	724,087	28	14	40	17
